


Upstream view through one half of twin box culvert over Thetford River.

May 1955



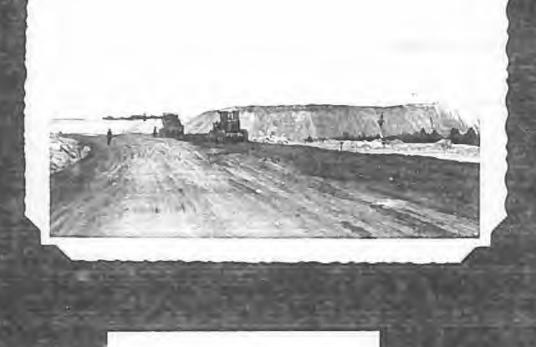

Laying gravel on North By-Pass.

May 26,1955

Tamping mill tailings around 8-inch asbestos cement water main on North By-Pass. BellBridge in background.

May 1955






Laying 8-inch asbestos cement water main on North By-Pass.


May 1955


North By-Pass under construction.Connection with Labranche Street.


May 1955




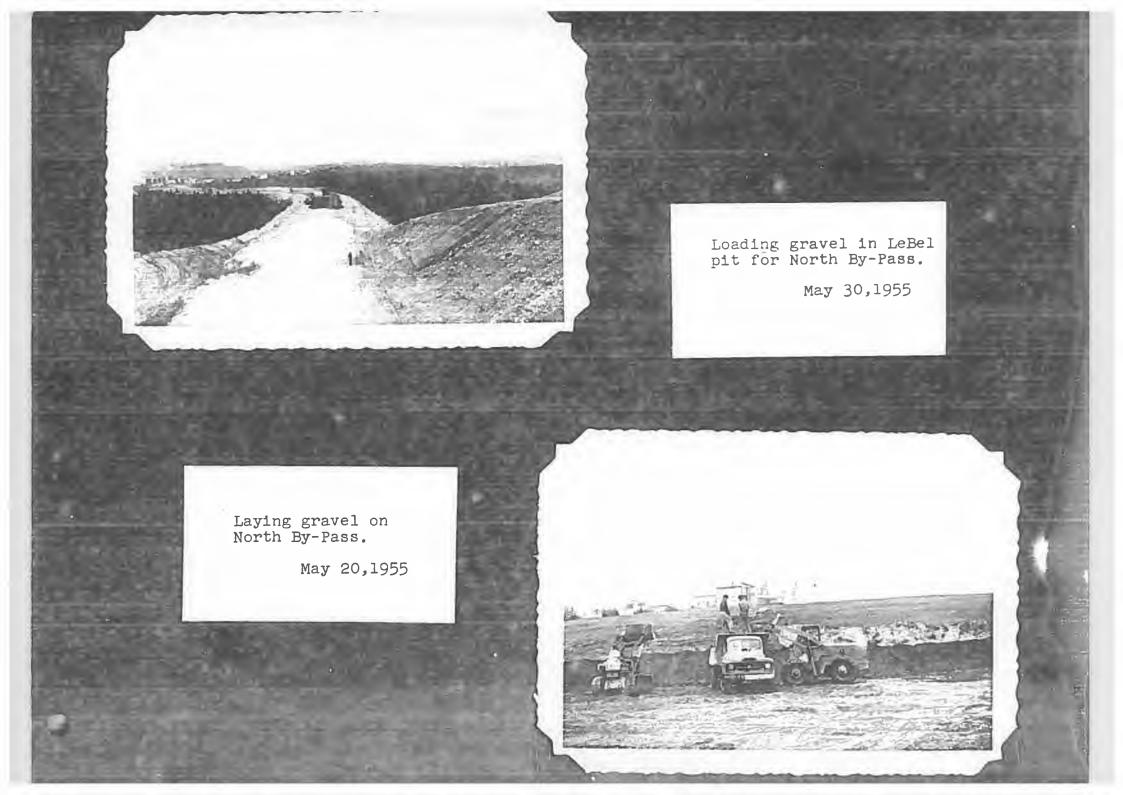


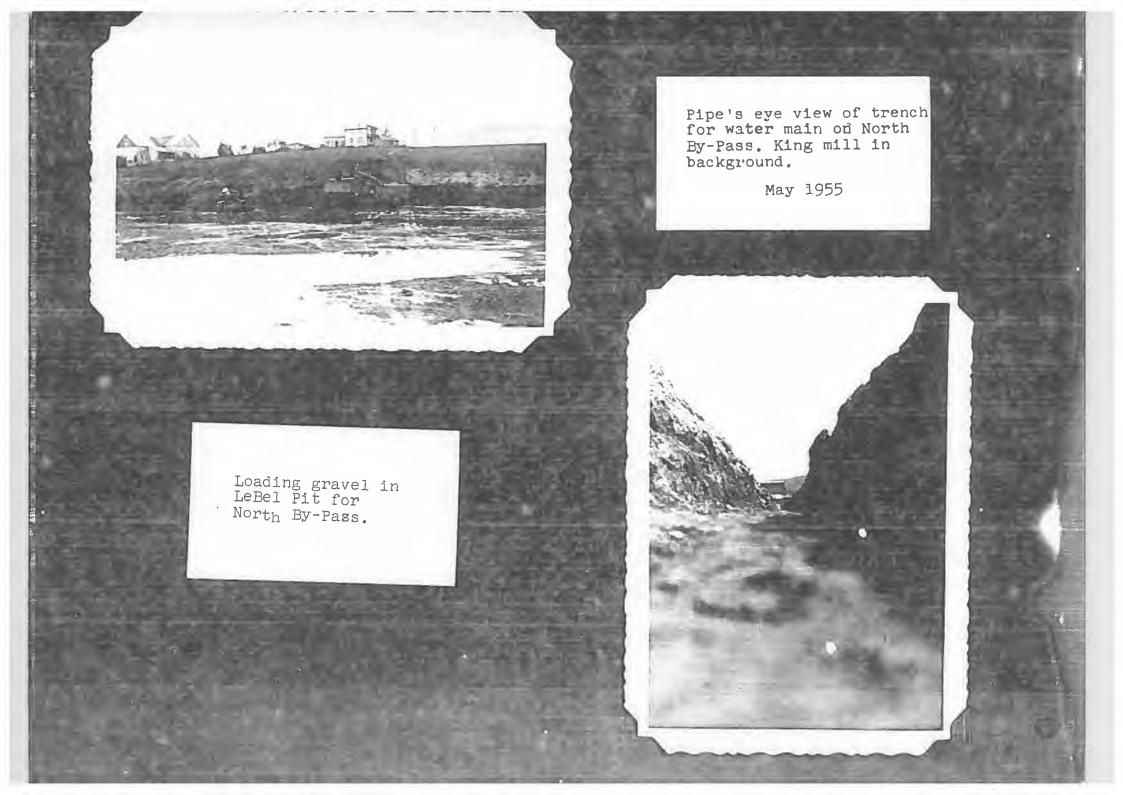

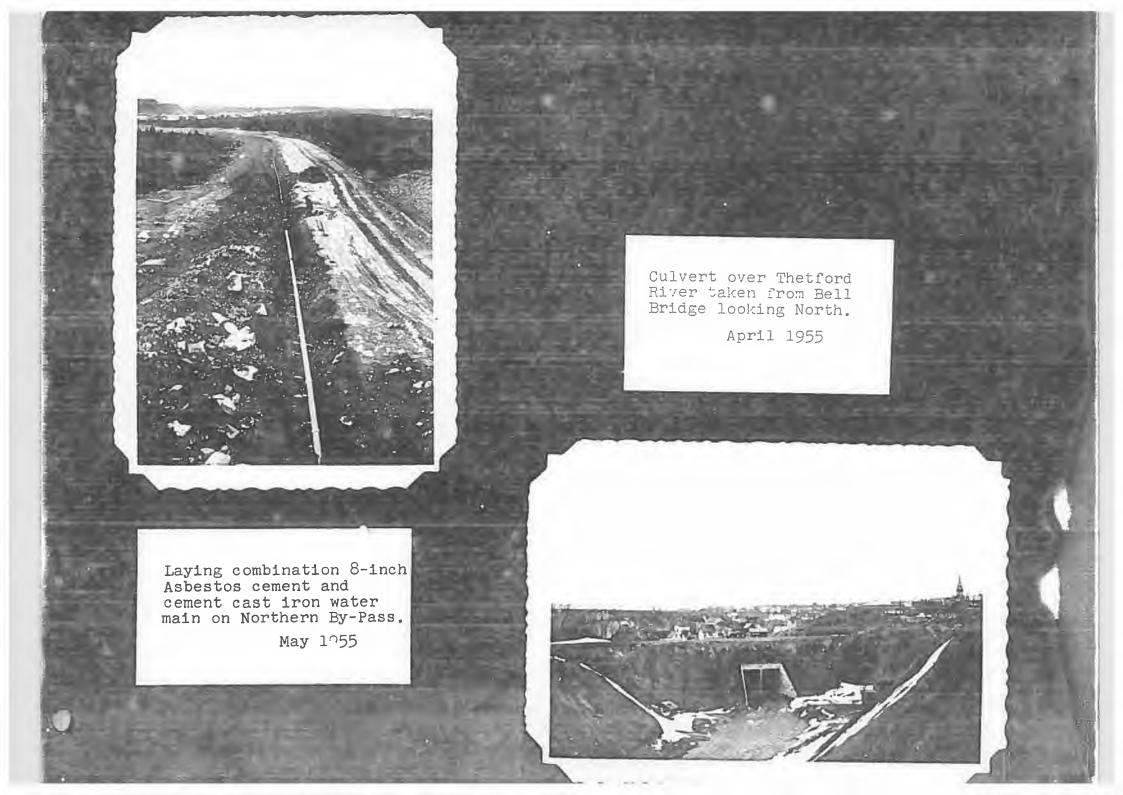

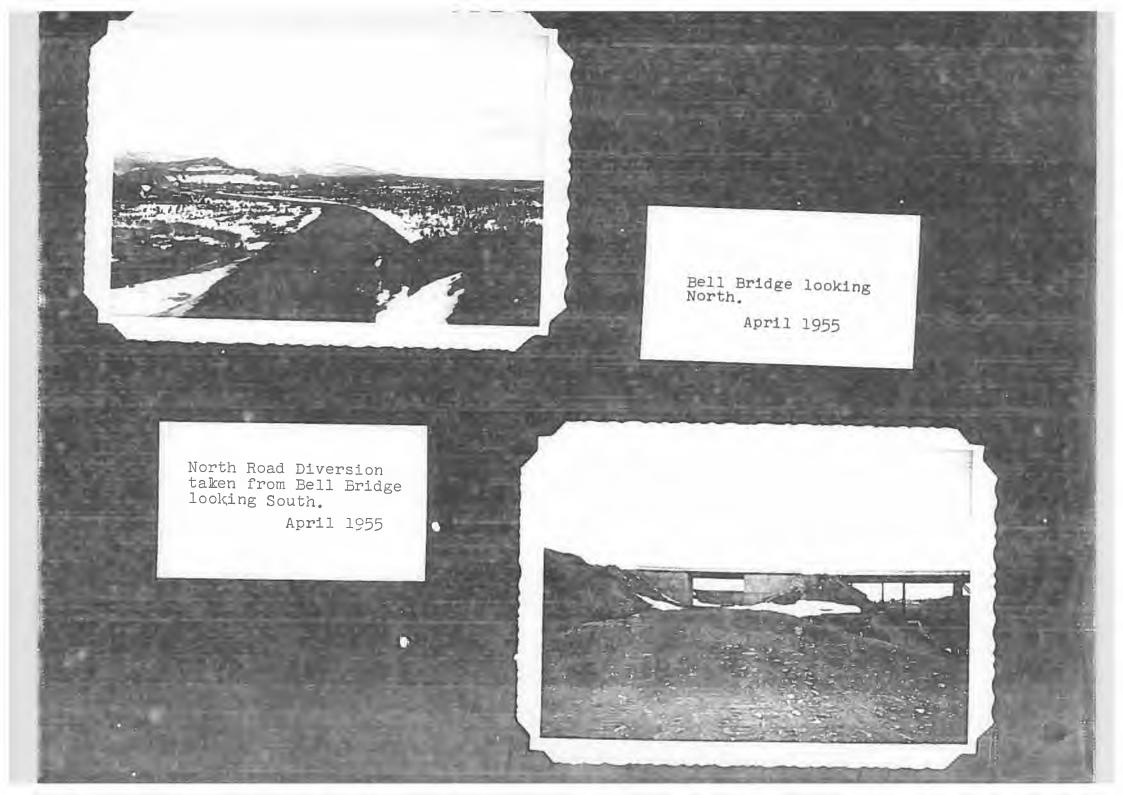

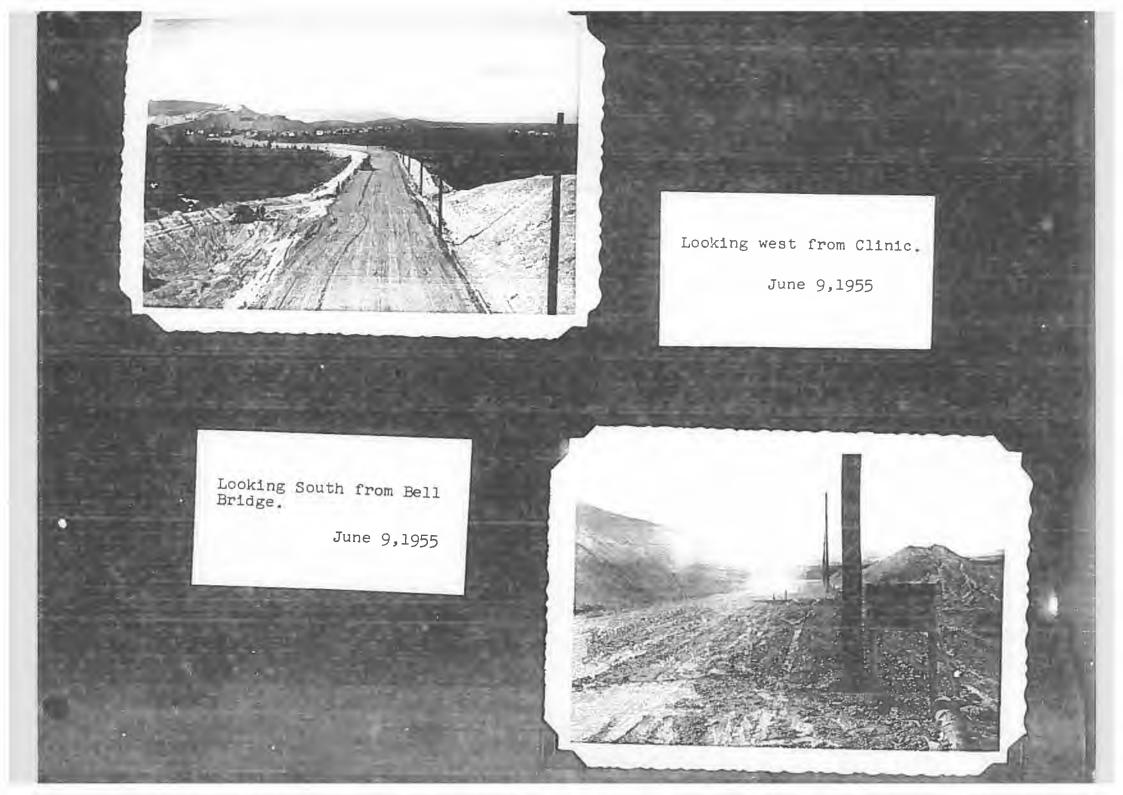

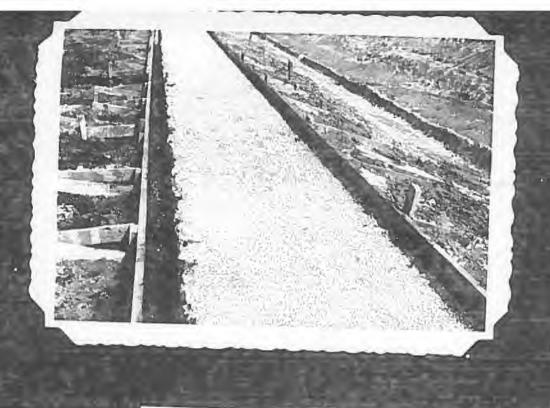

Showing stone and gravel foundation for sidewalk

June 16,1955

Showing construction of sidewalks screened coarse mill tailings over 4-inch crushed stone.

June16,55





Construction of masonry wall behind the Charest house.

July 6,1955

Pouring concrete for sidewalk.

June 16,1955





Cutting entry for St.Antoine.Entry for St.Francois
in background showing also
City construction of manhole.

July 6,1955

Trench for Bell Telephone cable by the Charest house.

July 6/55






Entry to St. Francois St., cut to rough grade.

July 6,1955

Cutting entry to St, Antoine Street.

July 6,1955



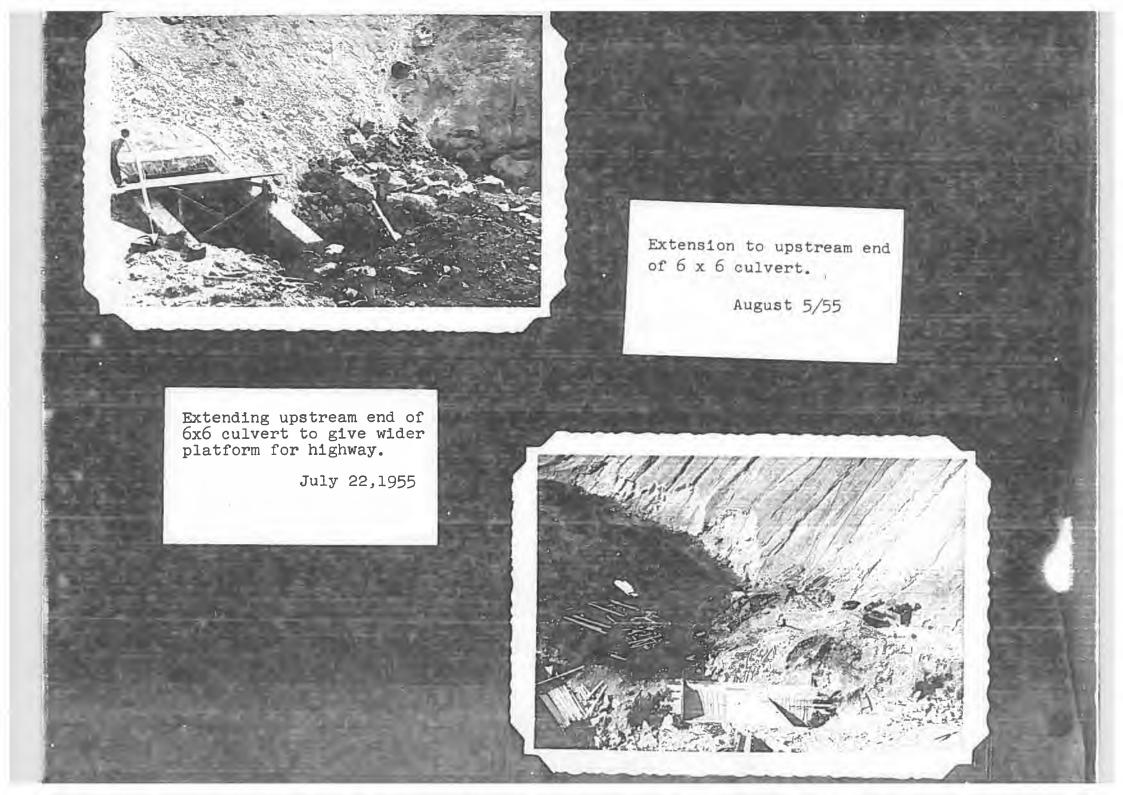




Start of paving operation

August 9,1955

Official Opening
August 9.1955



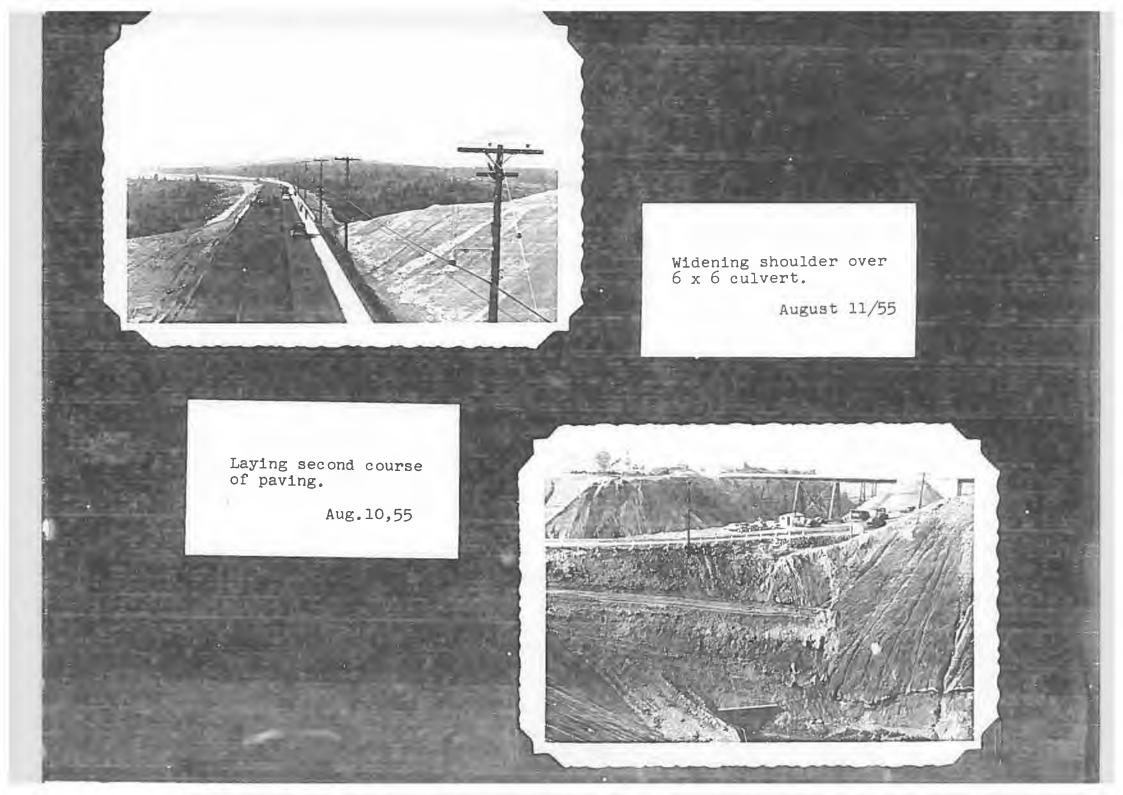




Excavation by Kennedy Construction of extention to St. Thomas St. Sept. 27/55

Widening shoulder over 6 x 6 culvert.

August 11,55



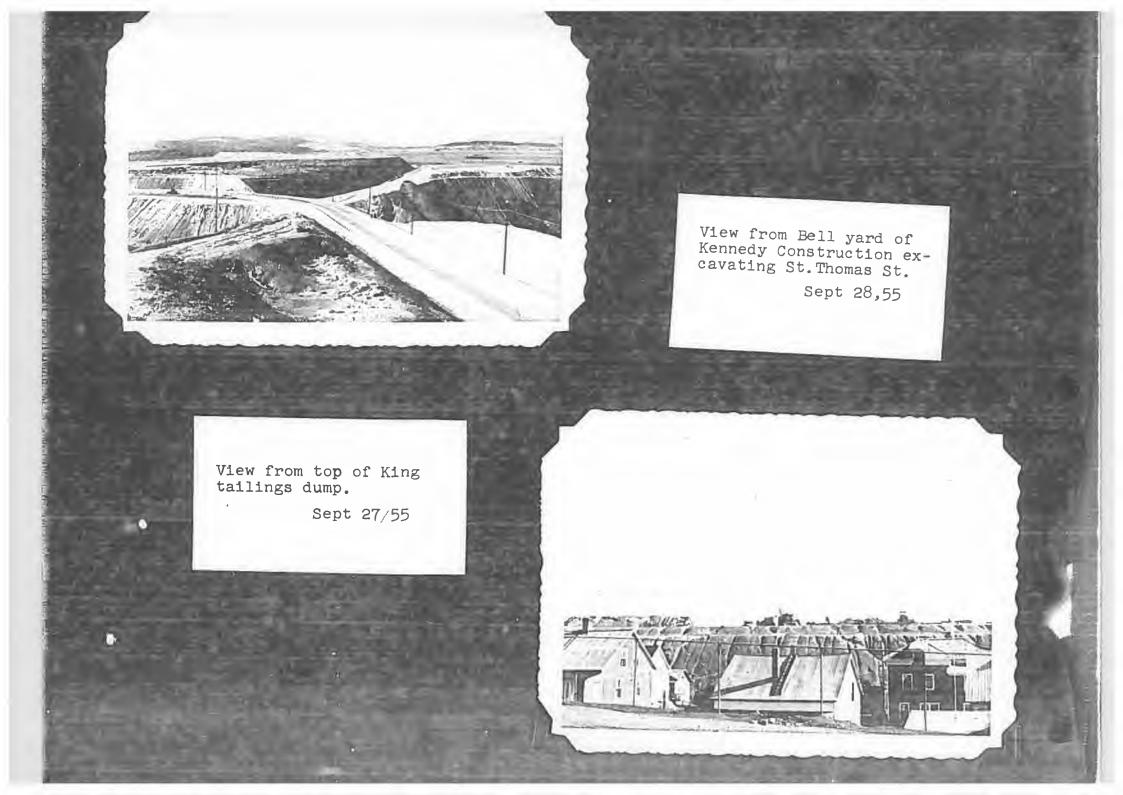




Curve on Pie Xl during paving.


July 31,56


Curve on Pie Xl immediately prior to paving.

July 31,56



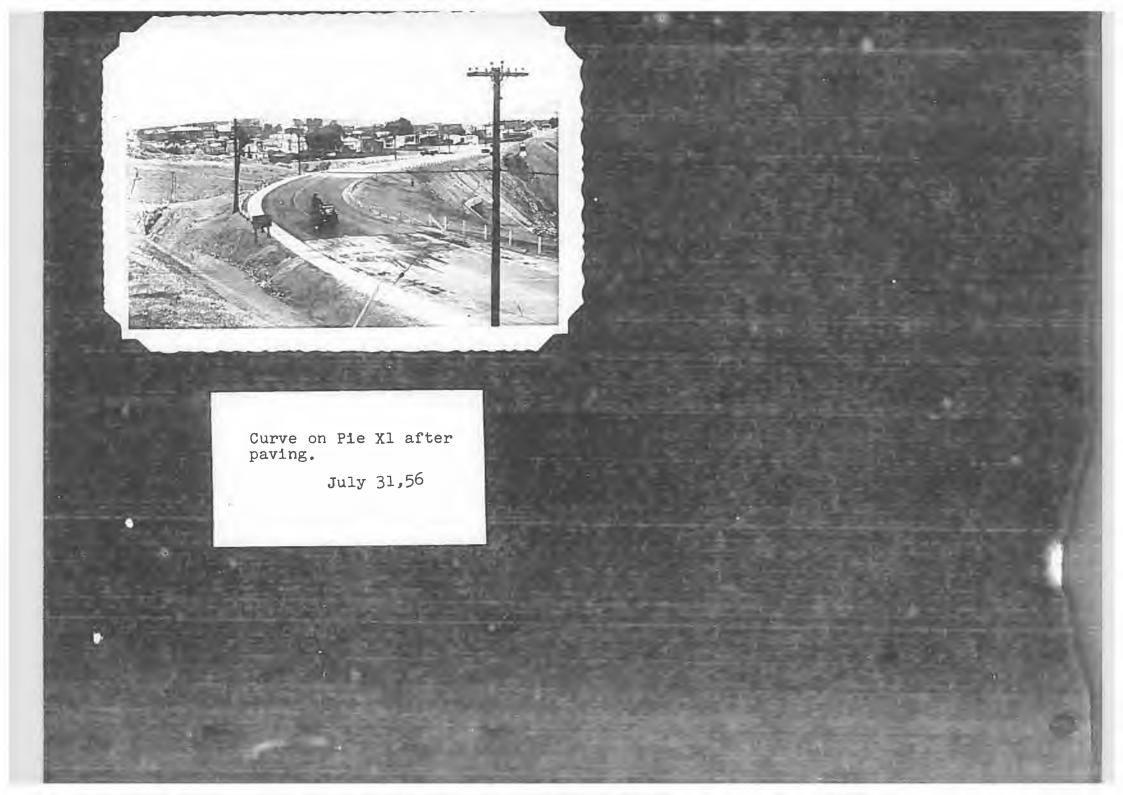

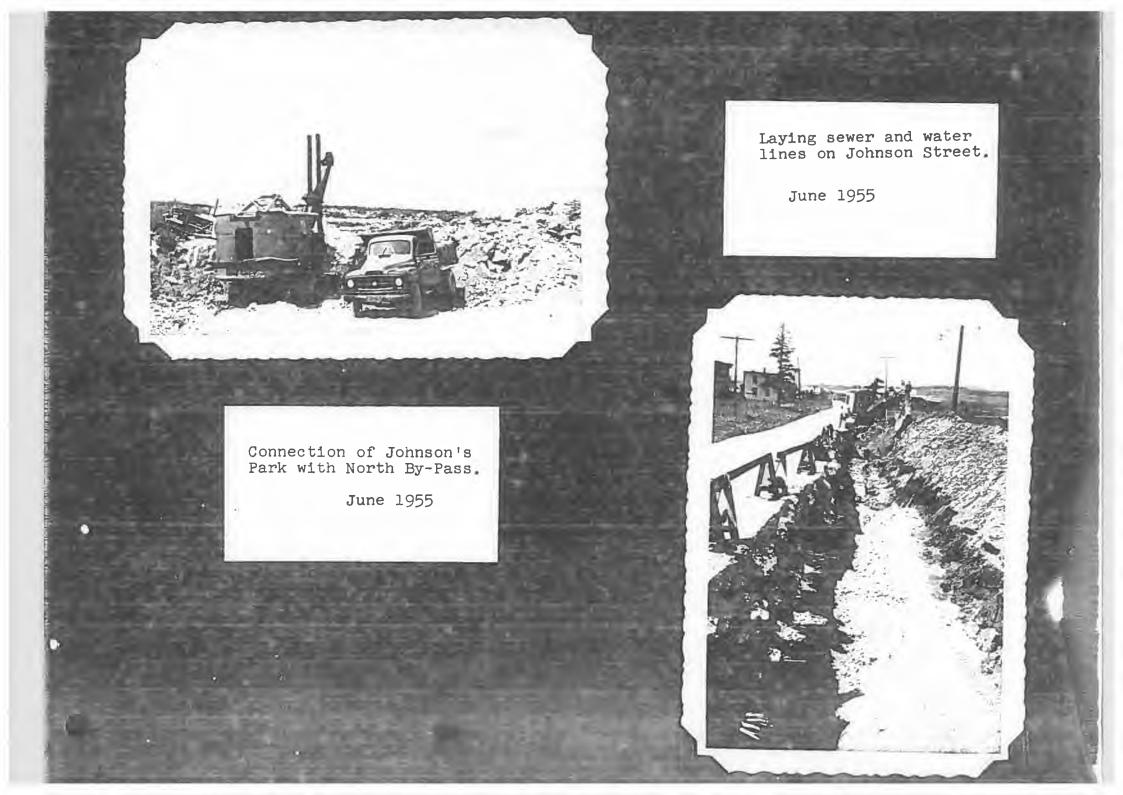

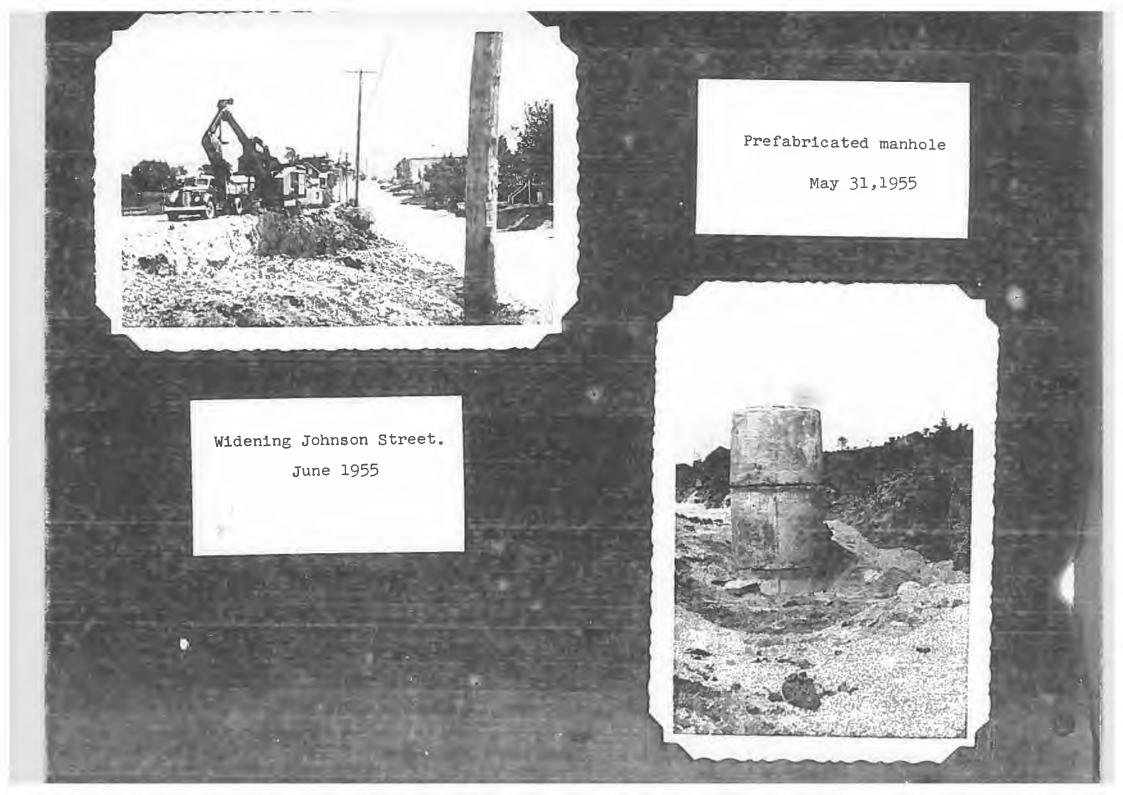



Atlas "Century" pipe to be installed. Class 150 6-inch & 8-inch.

May 31,55

Centre Street.

May 31,1955







Johnson's Park development.

May 23,1955

May 31,1955



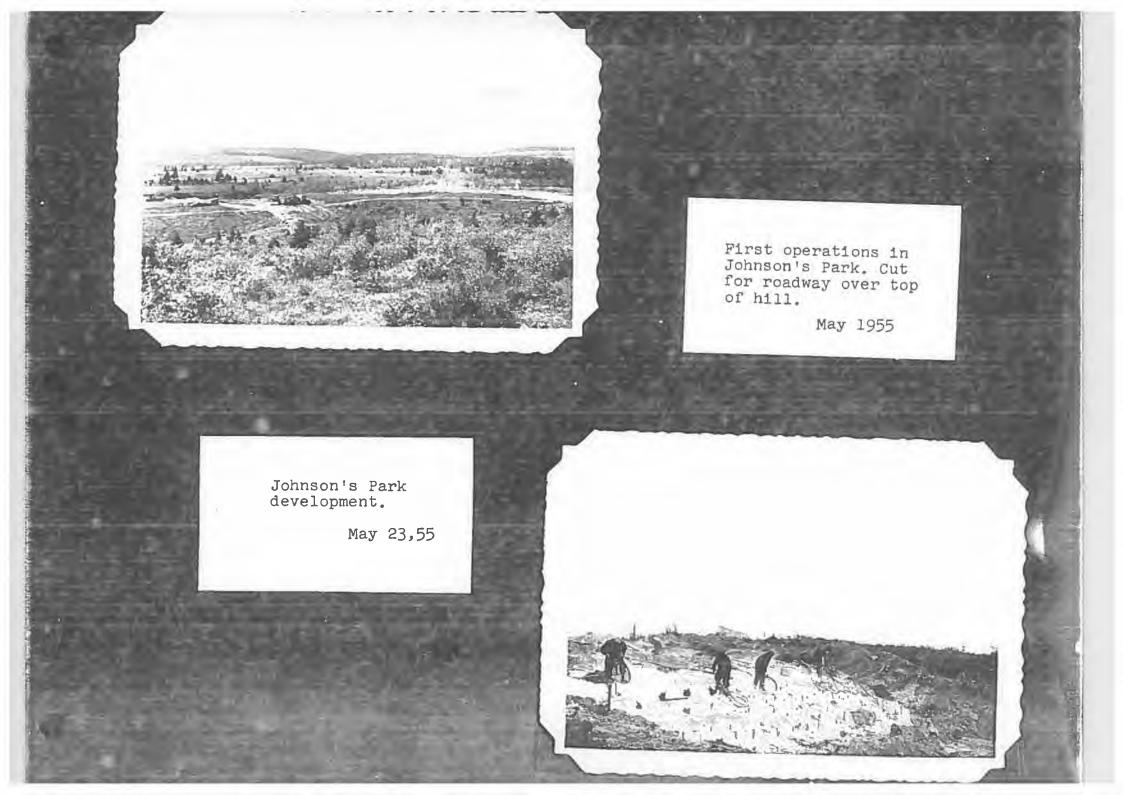

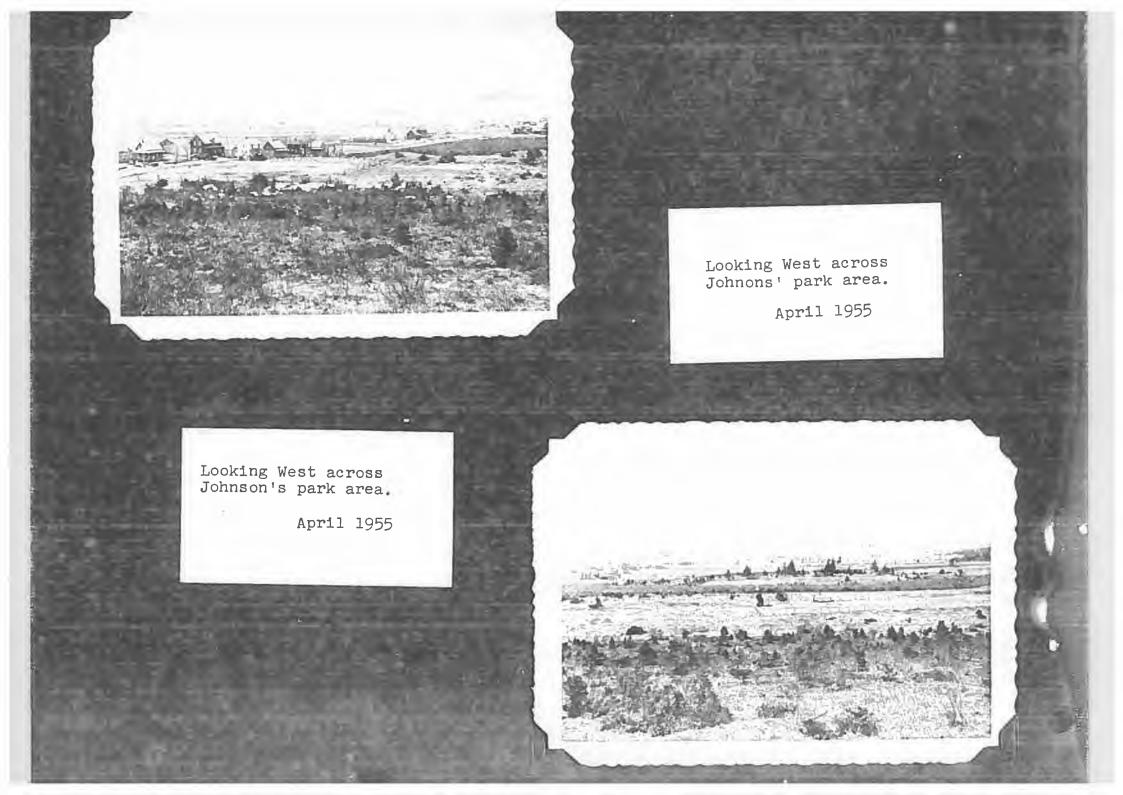




Laying 24-inch sewer on "Centre Street"Rock subgrade for street in foreground.

June 17.55

Excavation for roadways.

June 8,1955



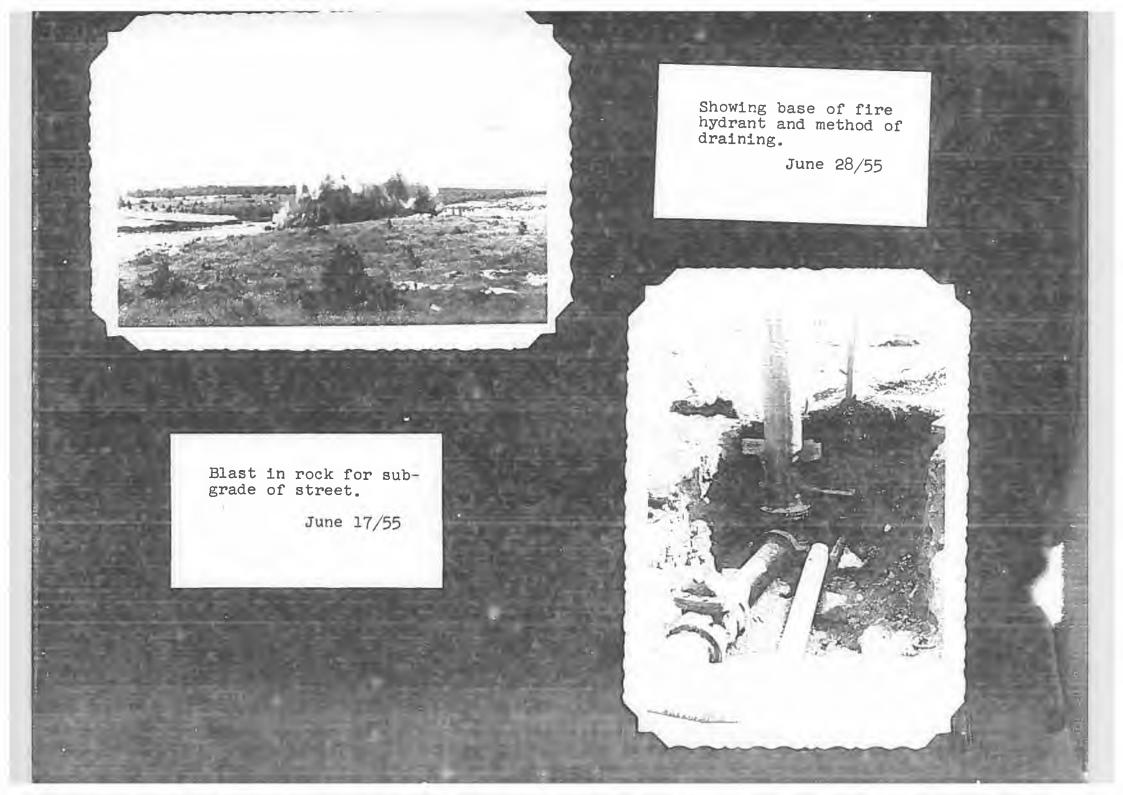



Showing domestic lines for water and sewage.

June 28/55





8-inch waterline connection and sewer junction at upper end of "Center St.:"

June 29/55

Excavation for sewer pipe beneath 8-inch A.C. water line on North By-Pass.

July 4/55





Construction of catch basin.

June 28/55

June 28/55






Start of gravel pit at Black Lake to supply road gravel for Johnson's Park.


July 5/55


Showing base of catch basin water line connection to fire hydrant and sewer connection to base of manhole at top of sylvain street.


July 12/55



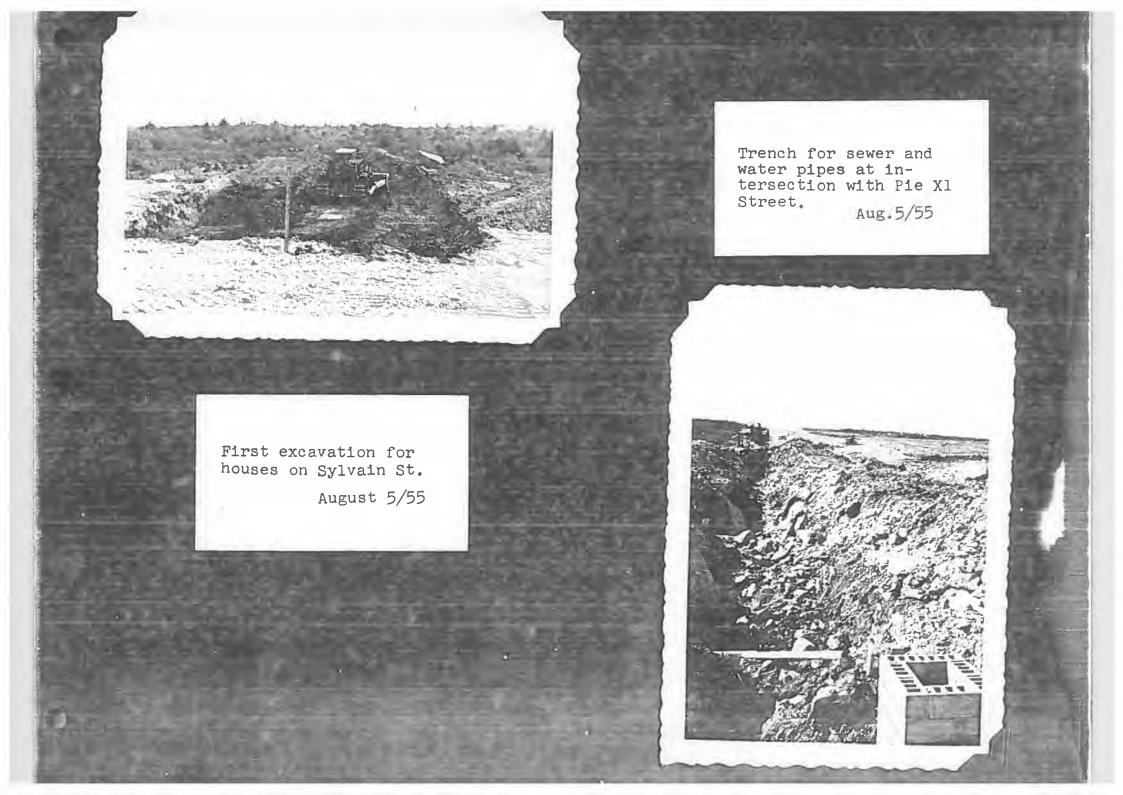


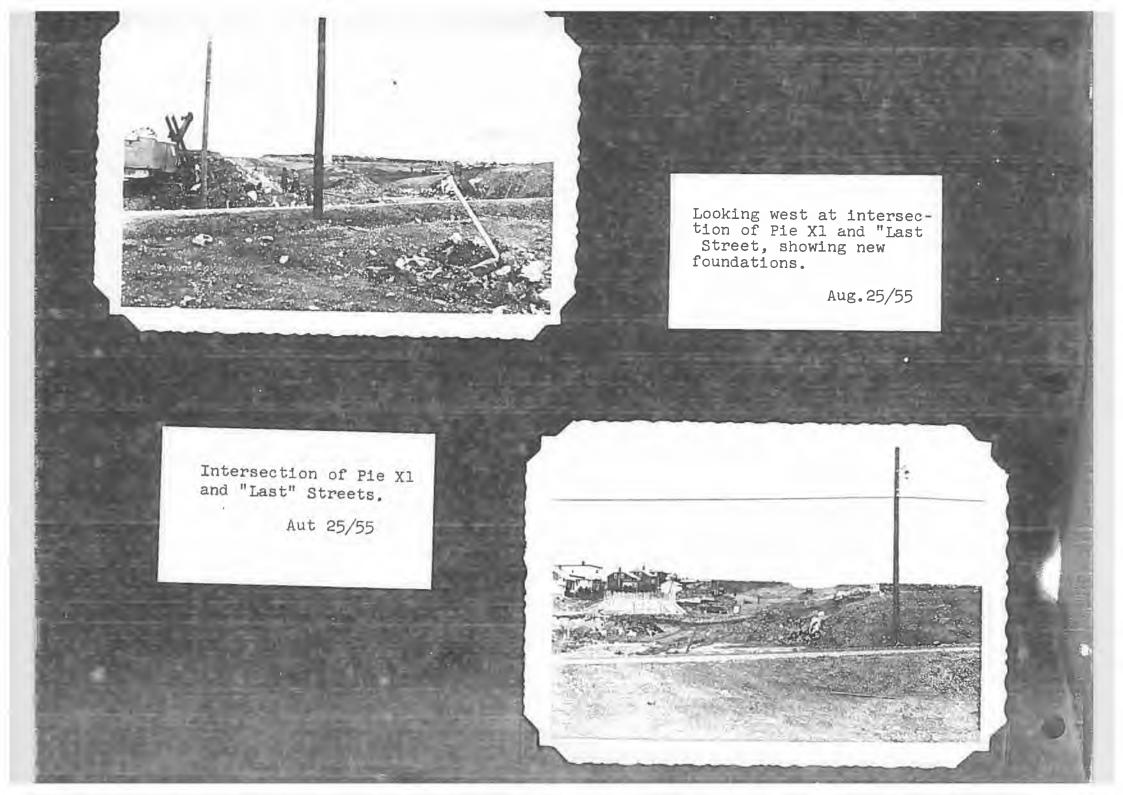


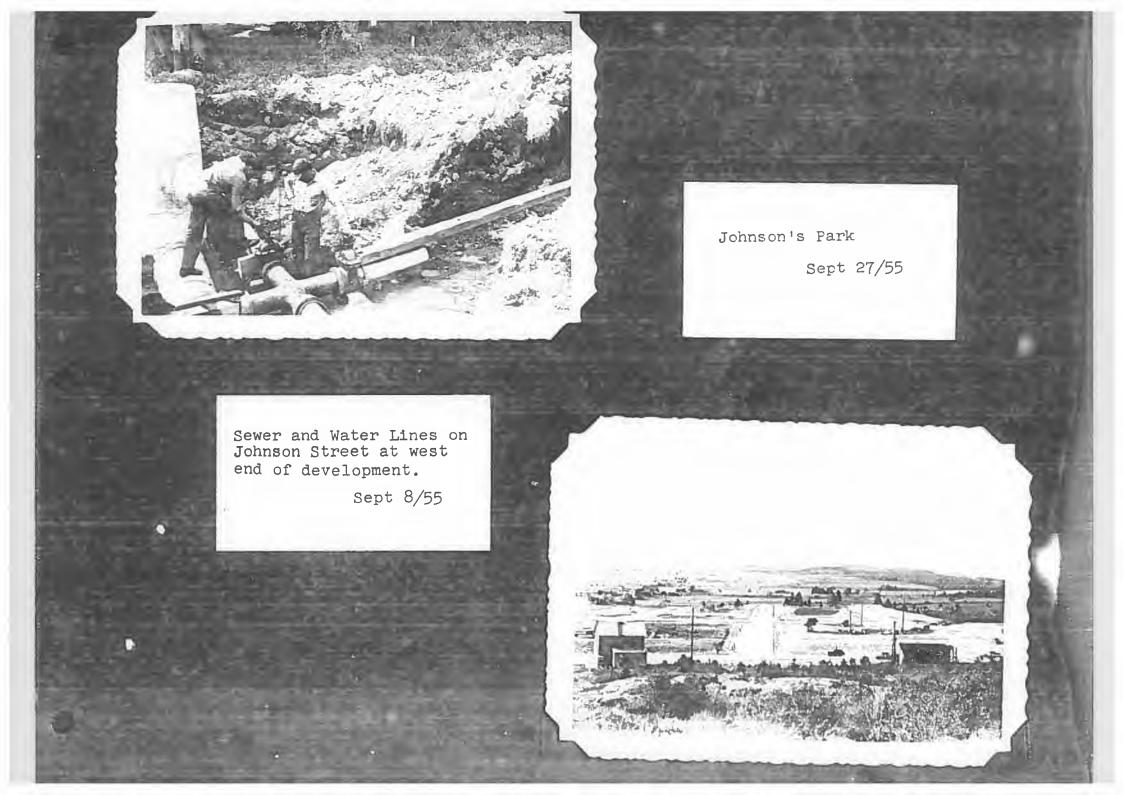


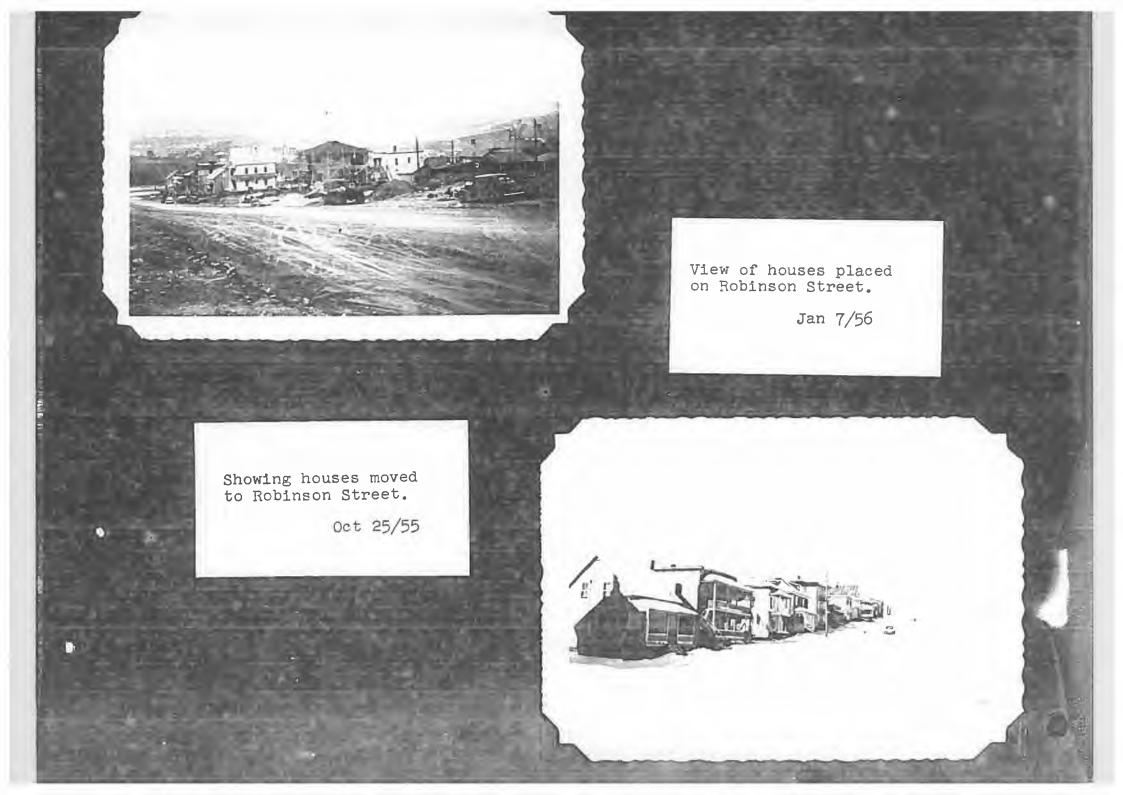



The Rebocation Project
The Aford Mines
V. 2.

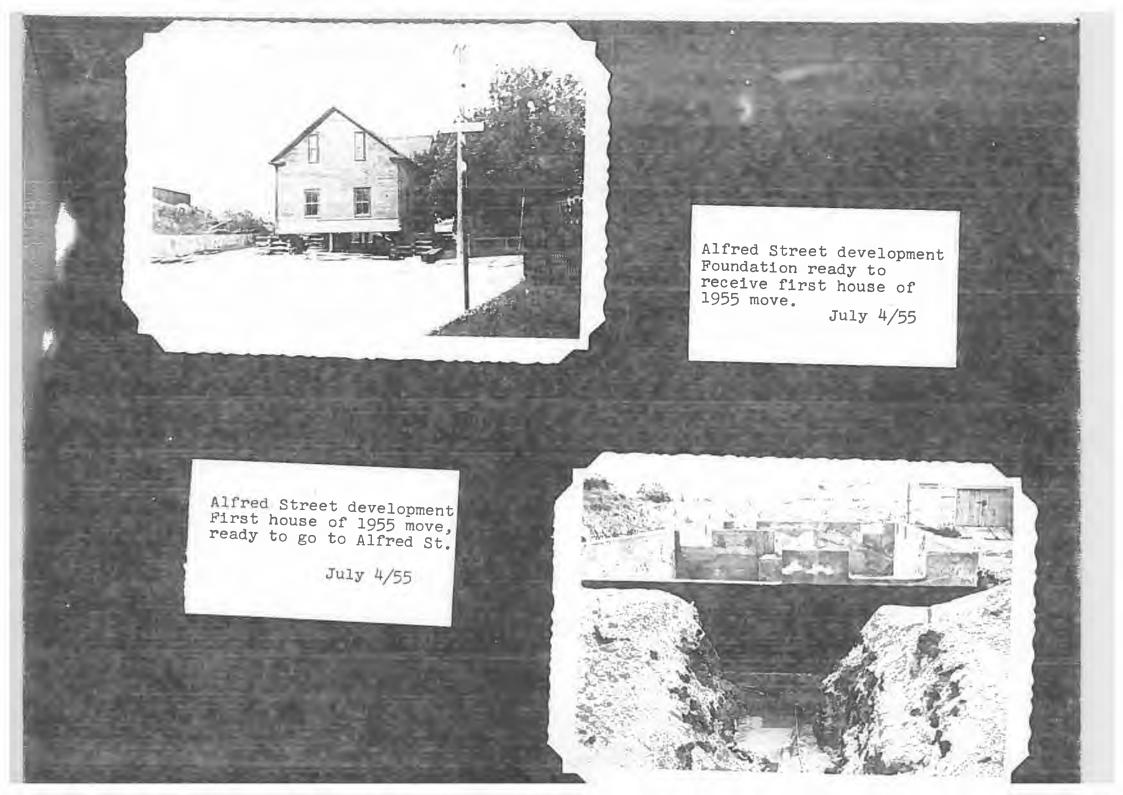


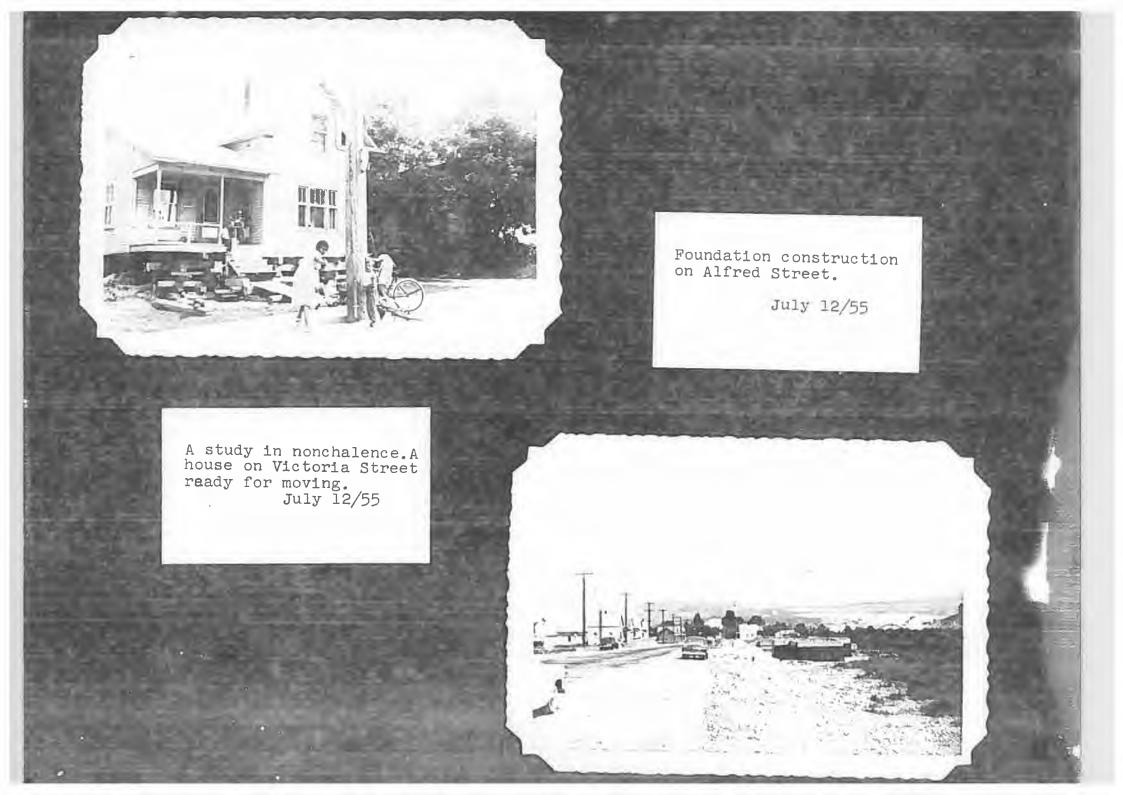


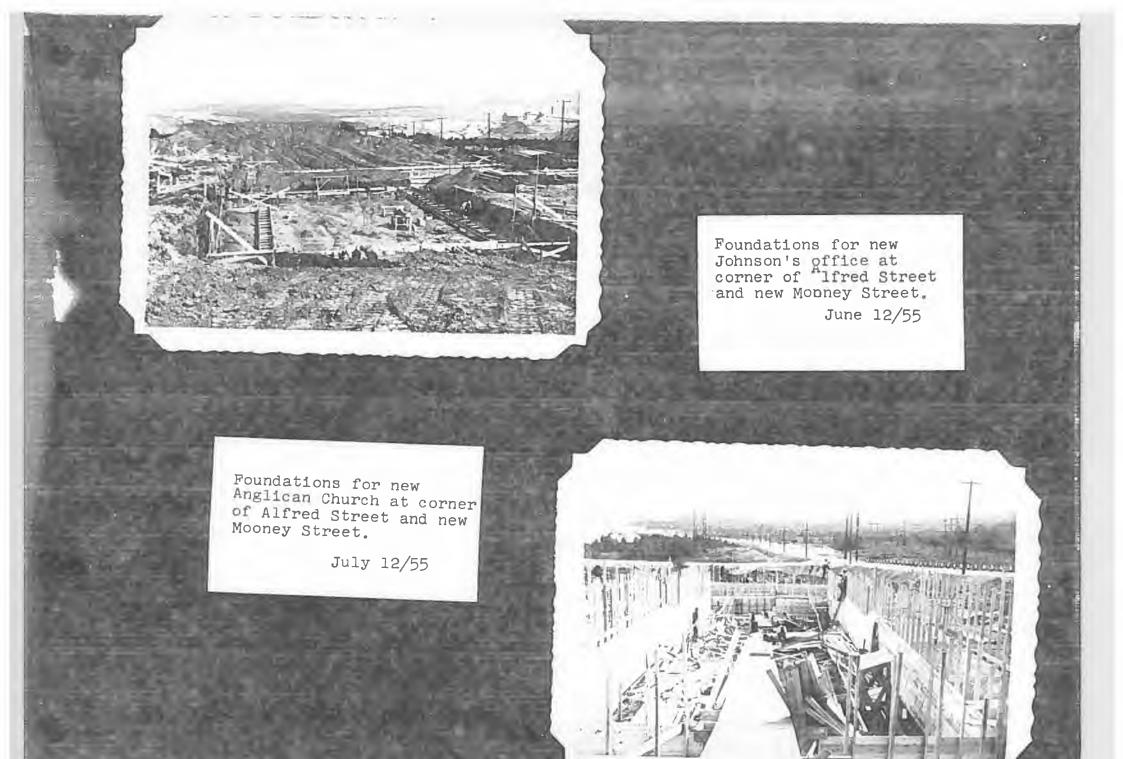


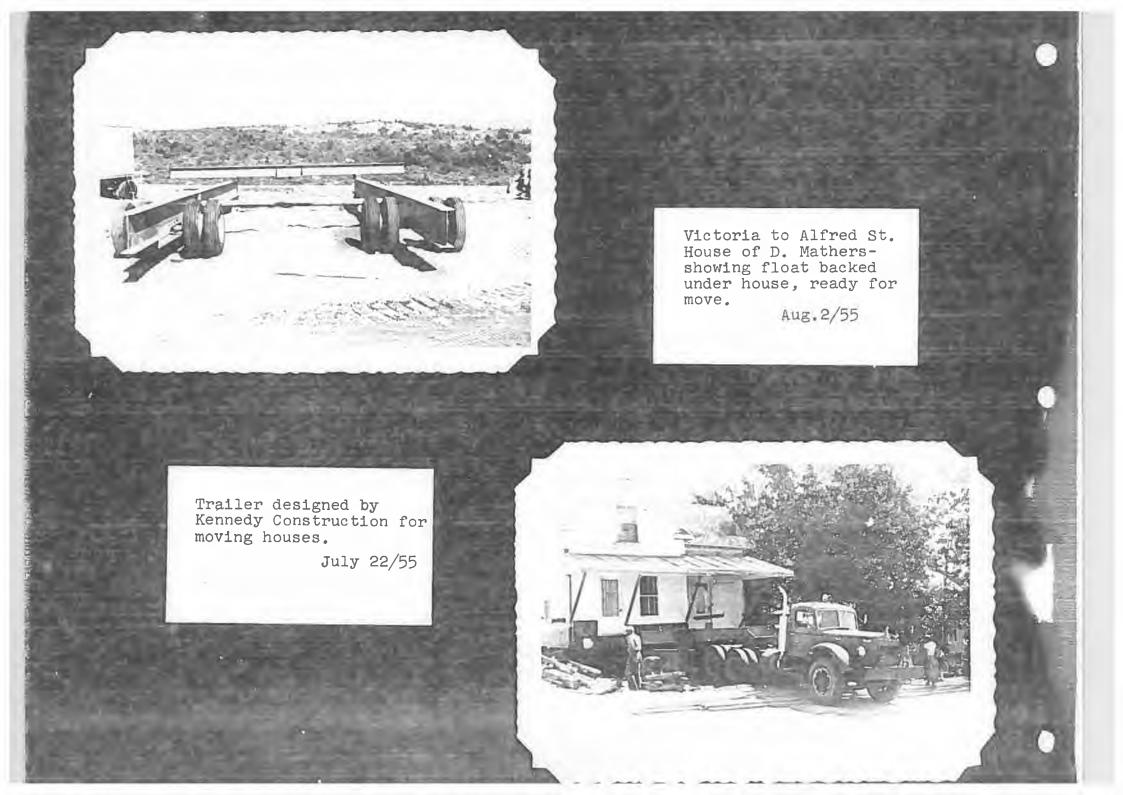


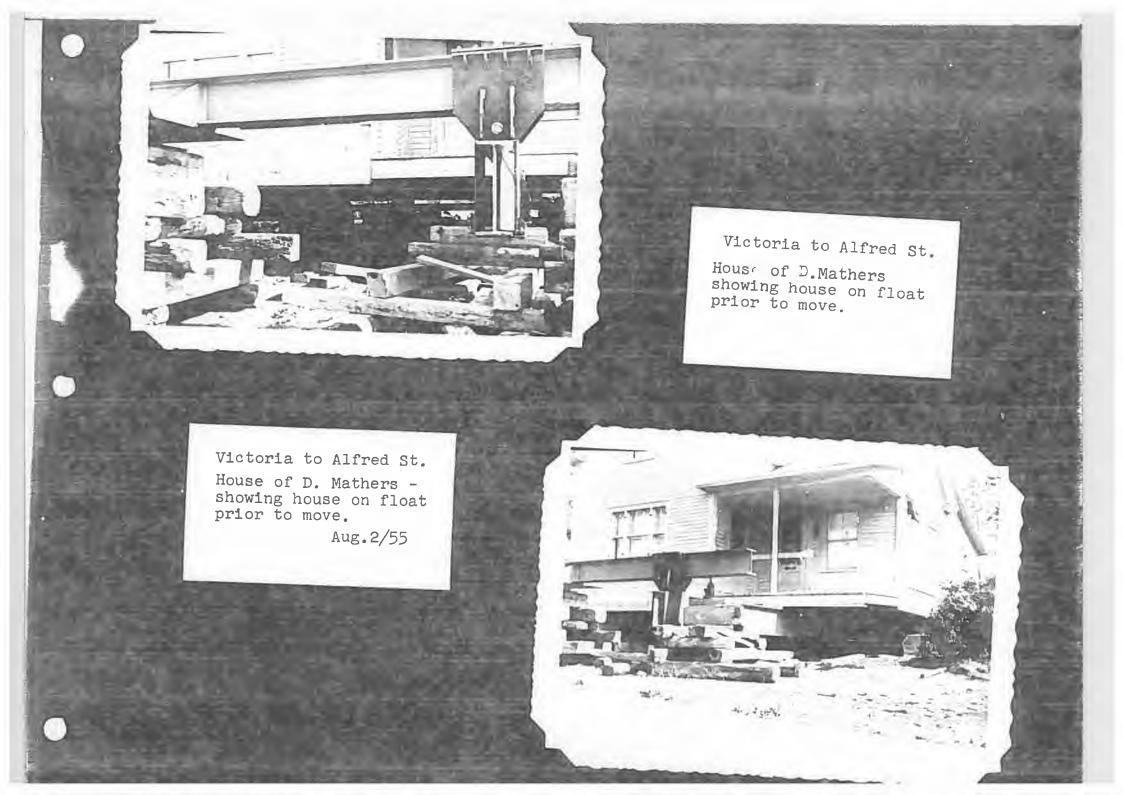


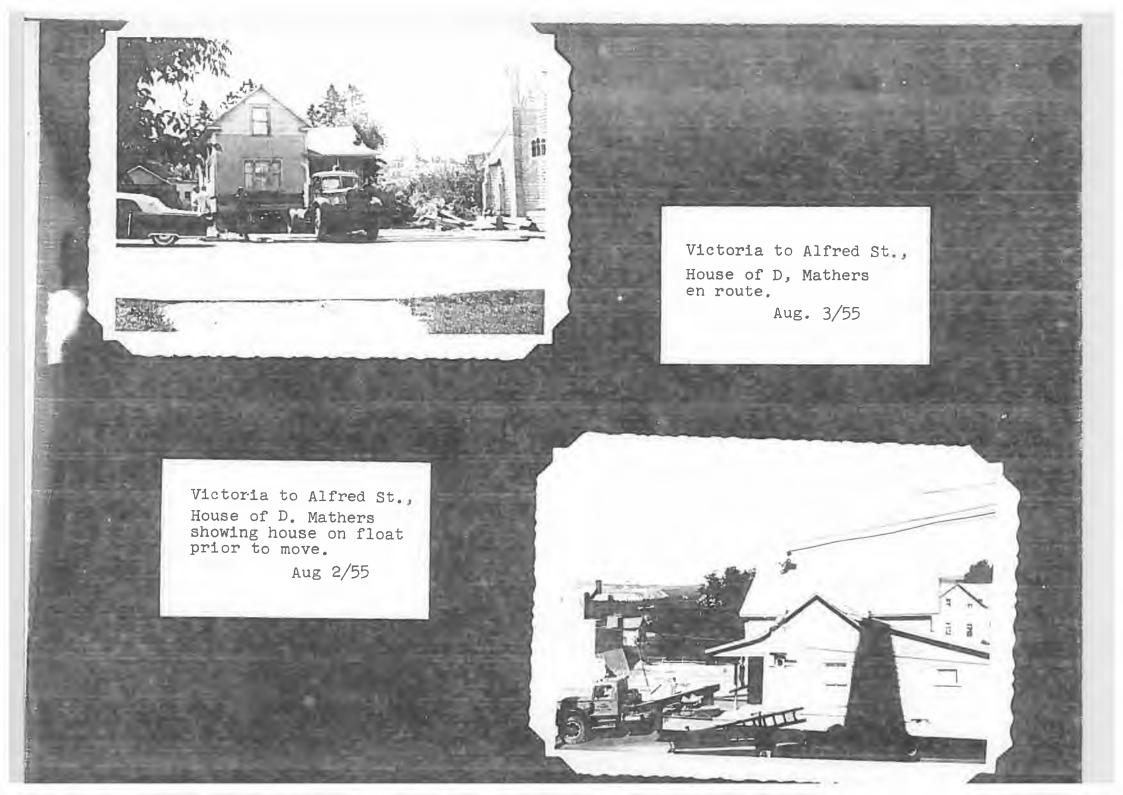


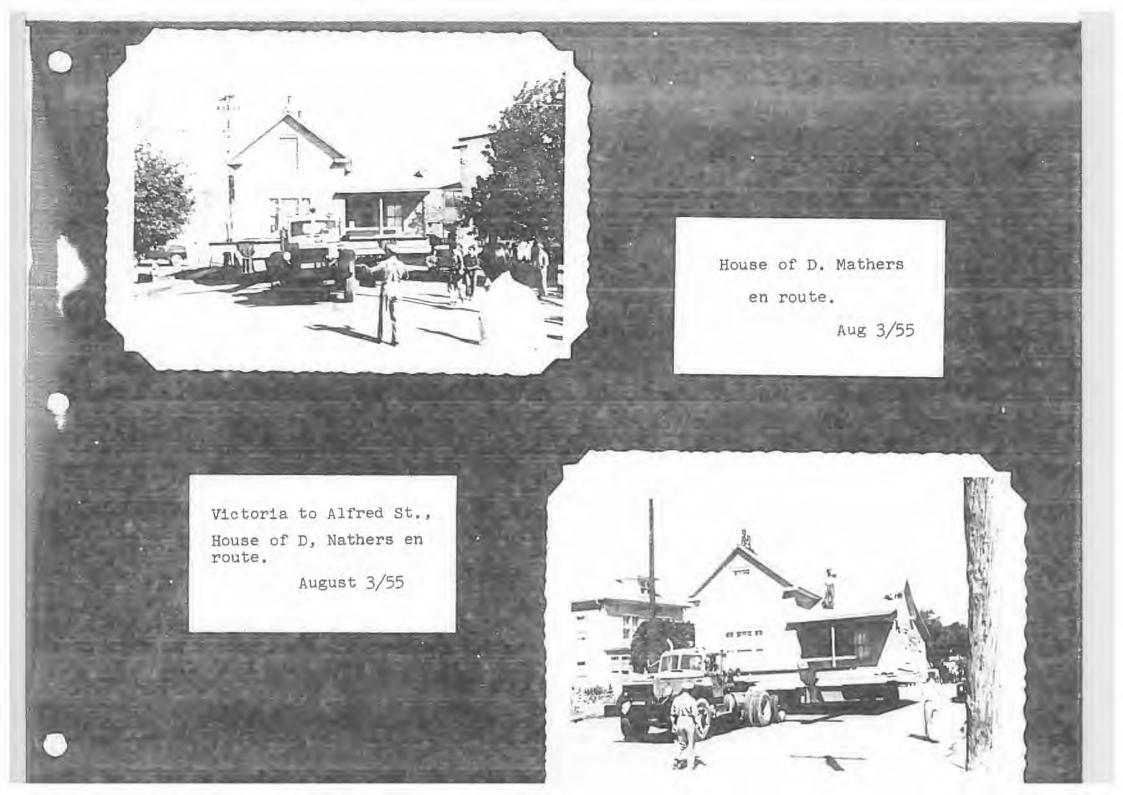


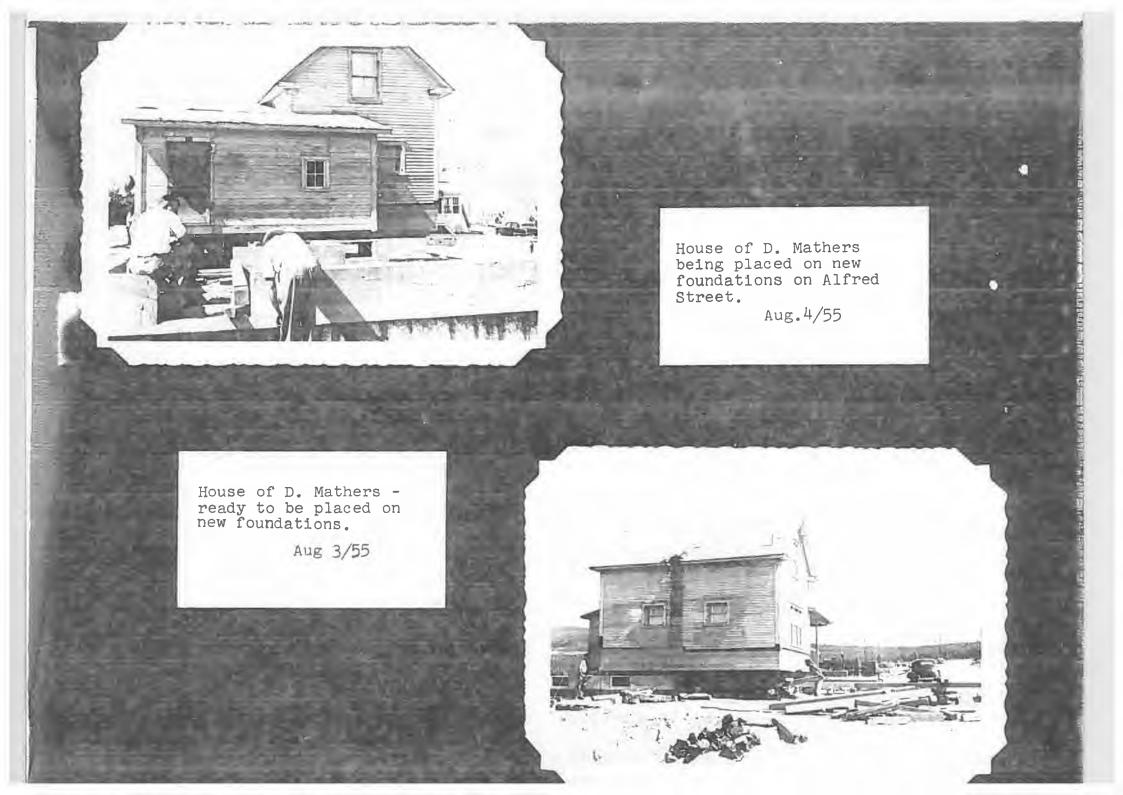


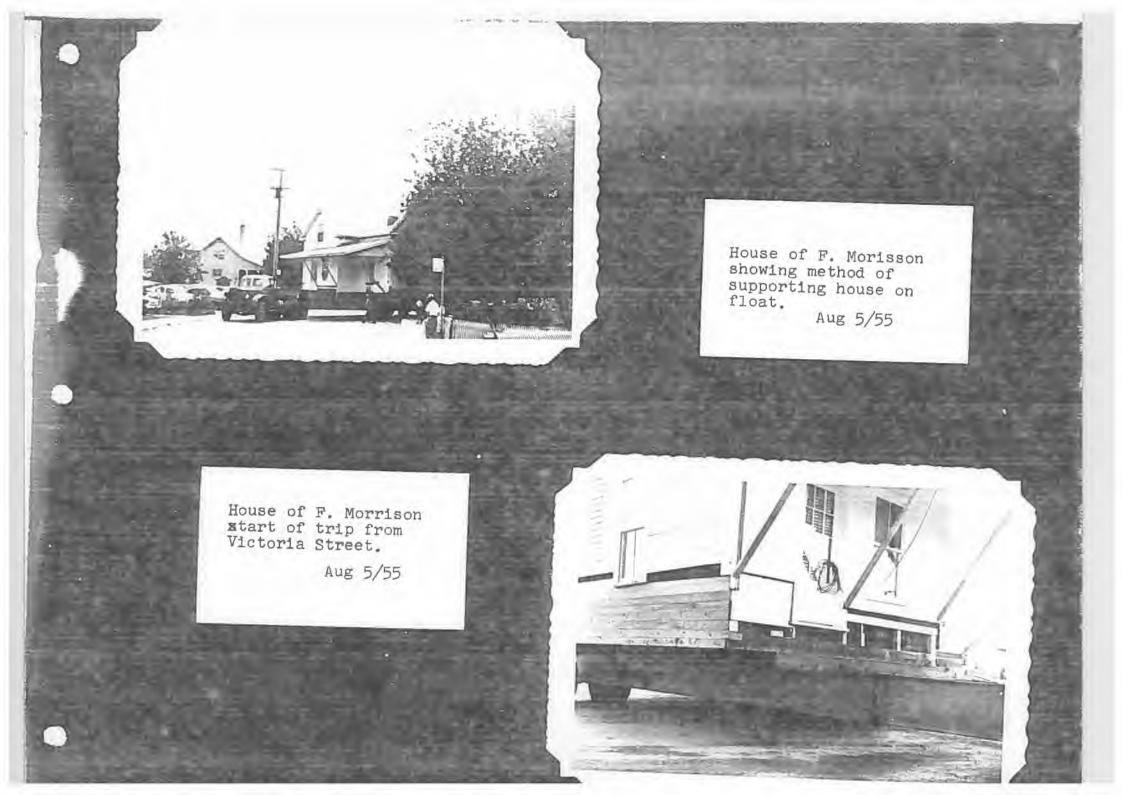


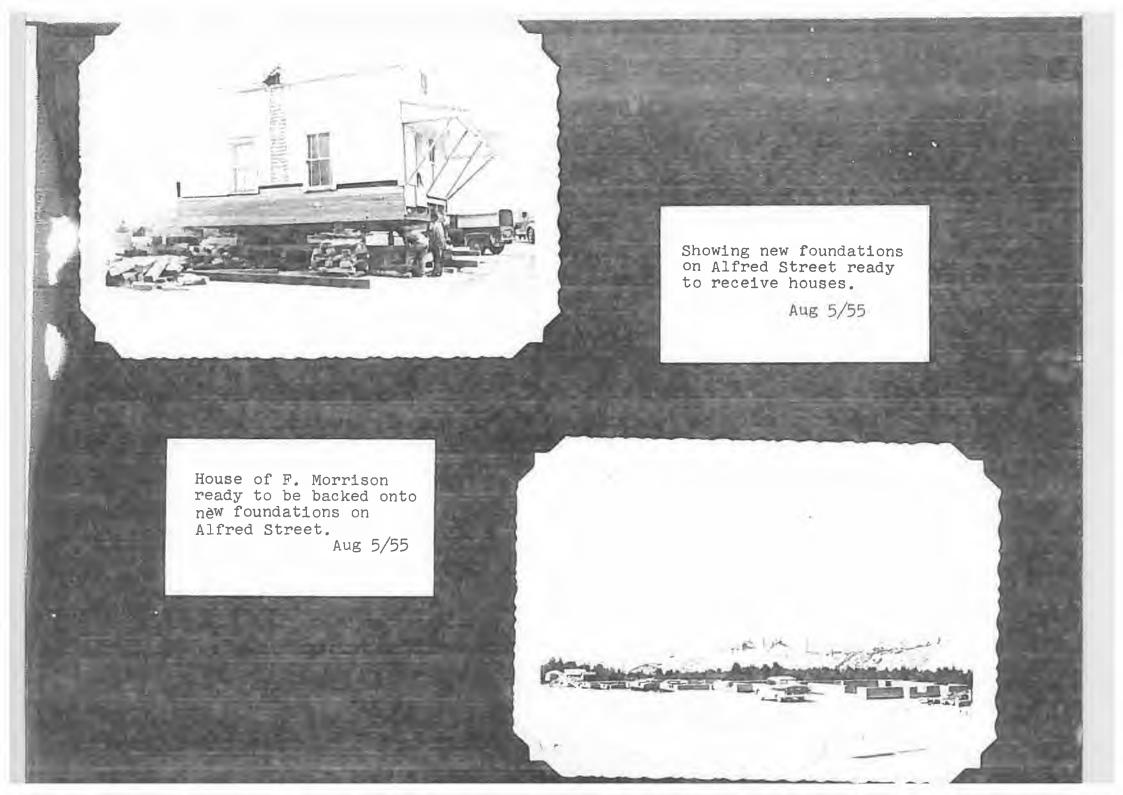


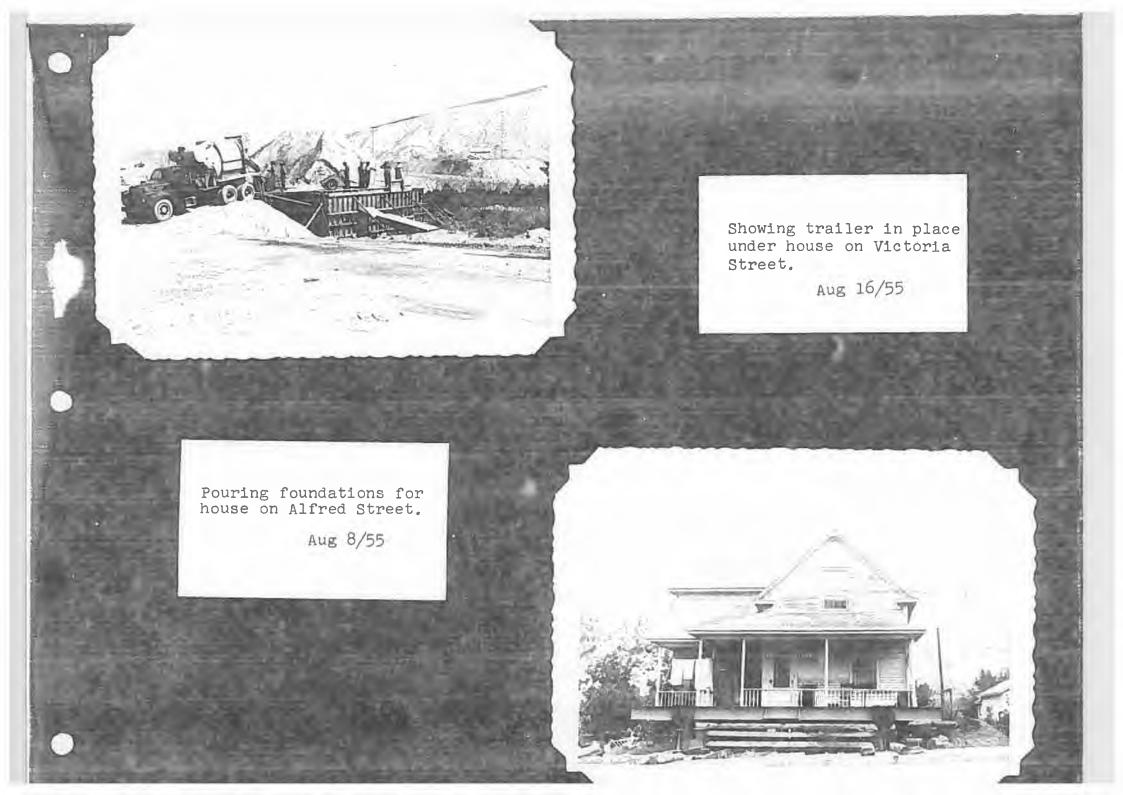


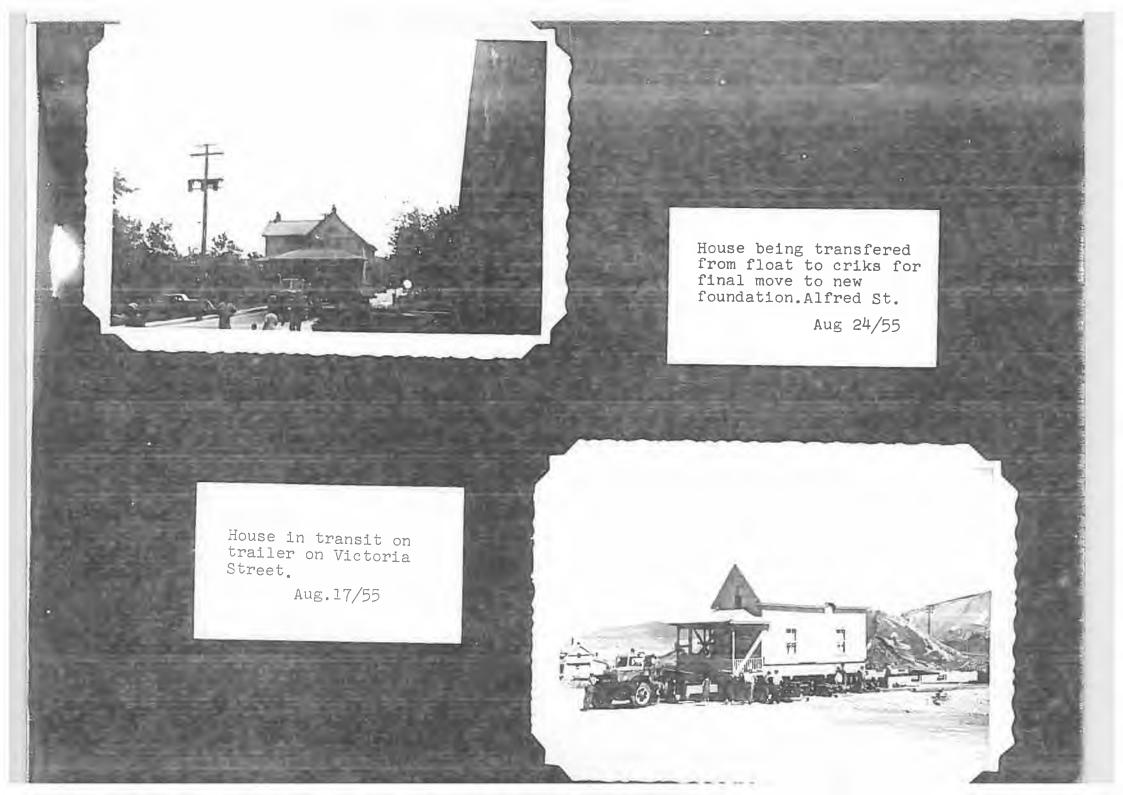

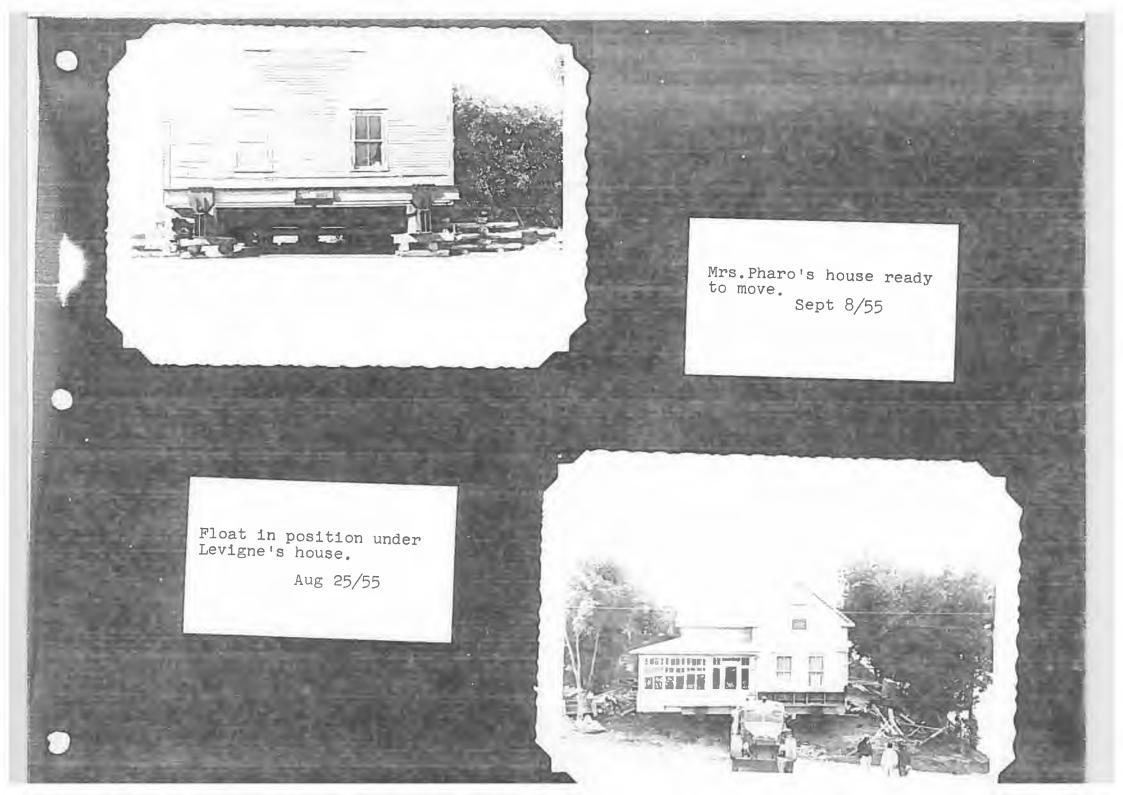


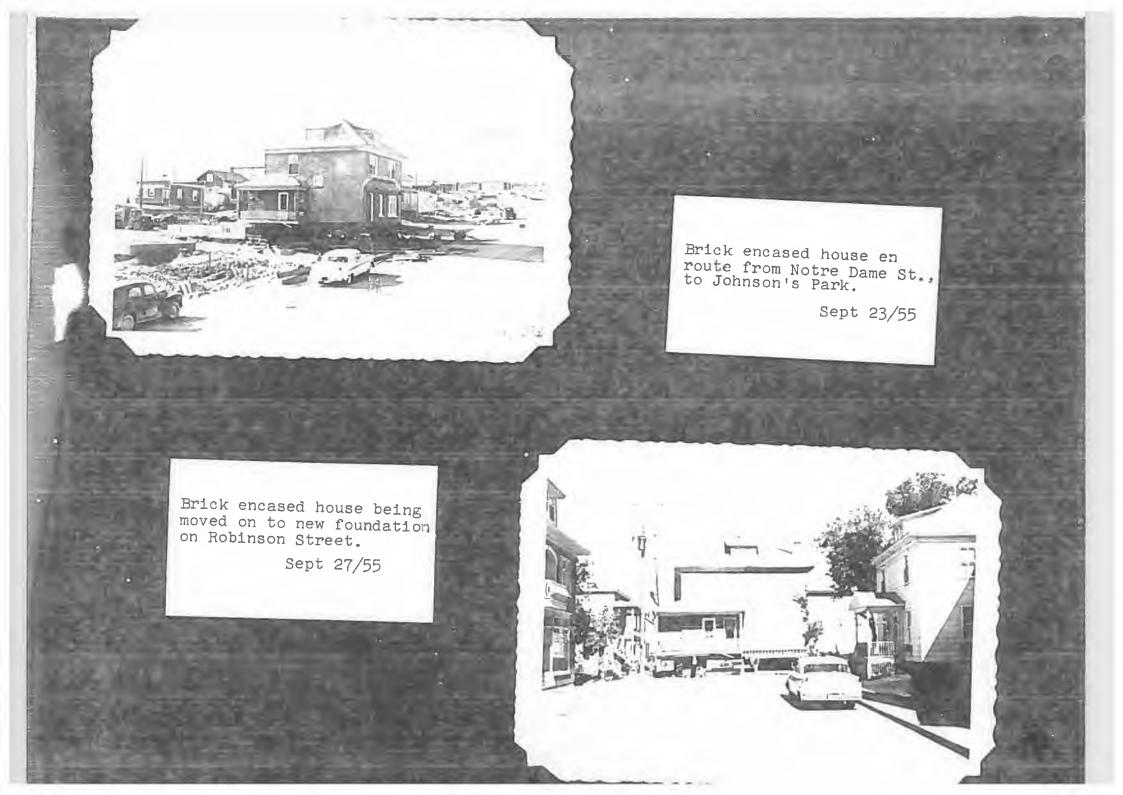


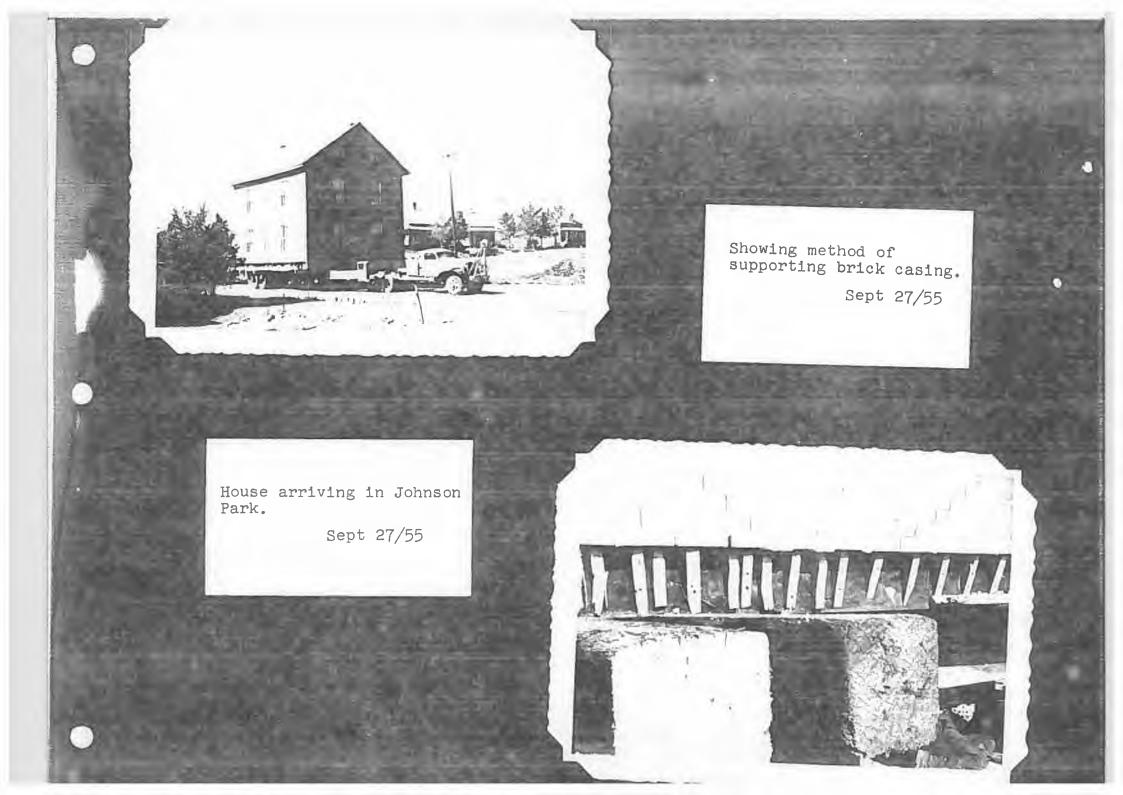


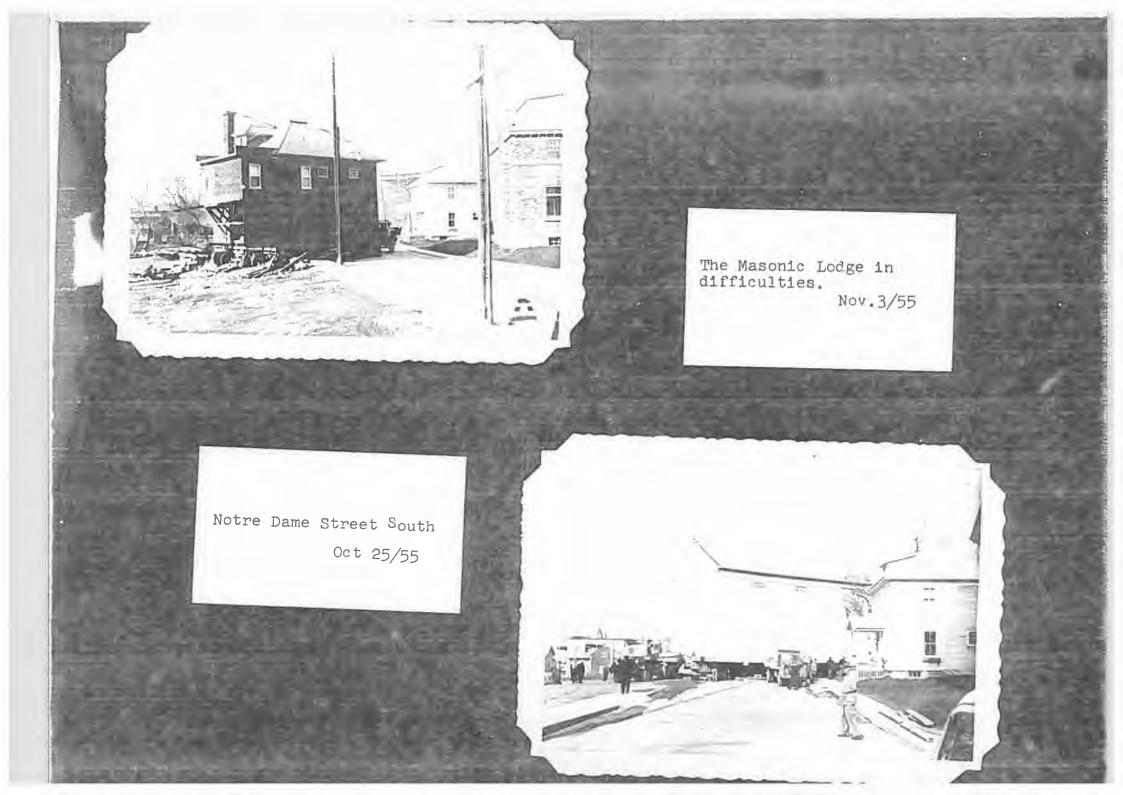





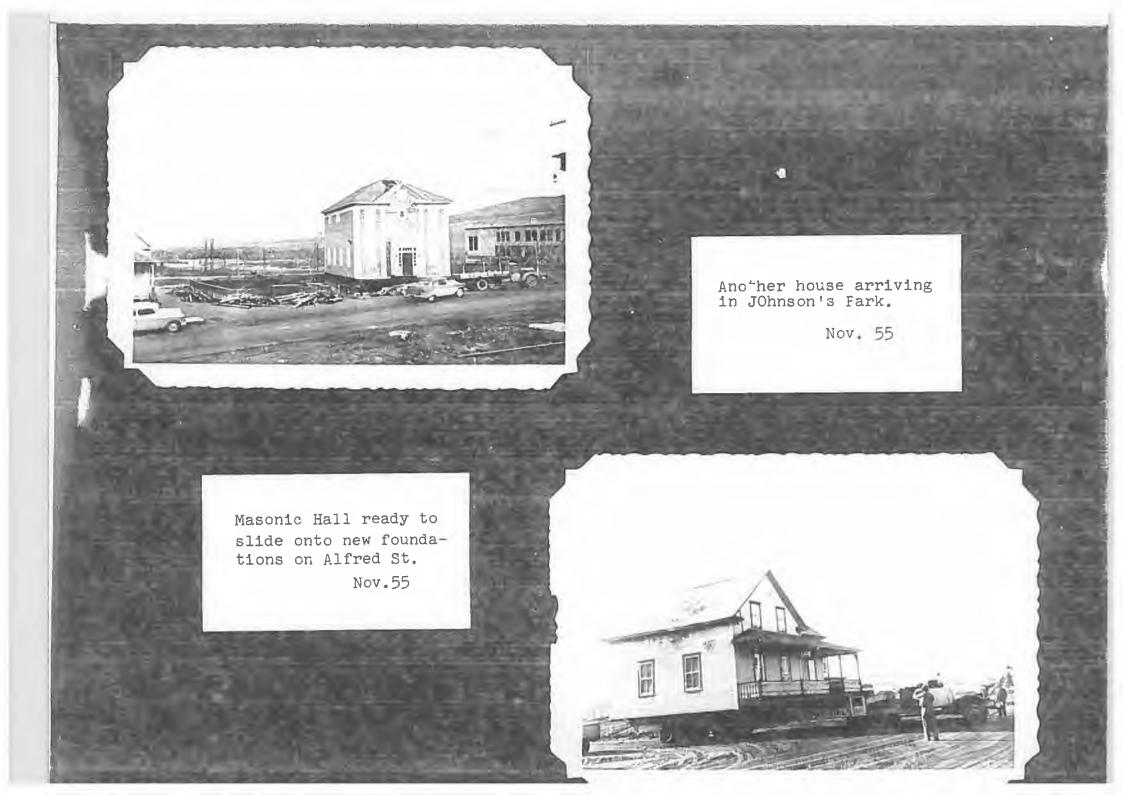


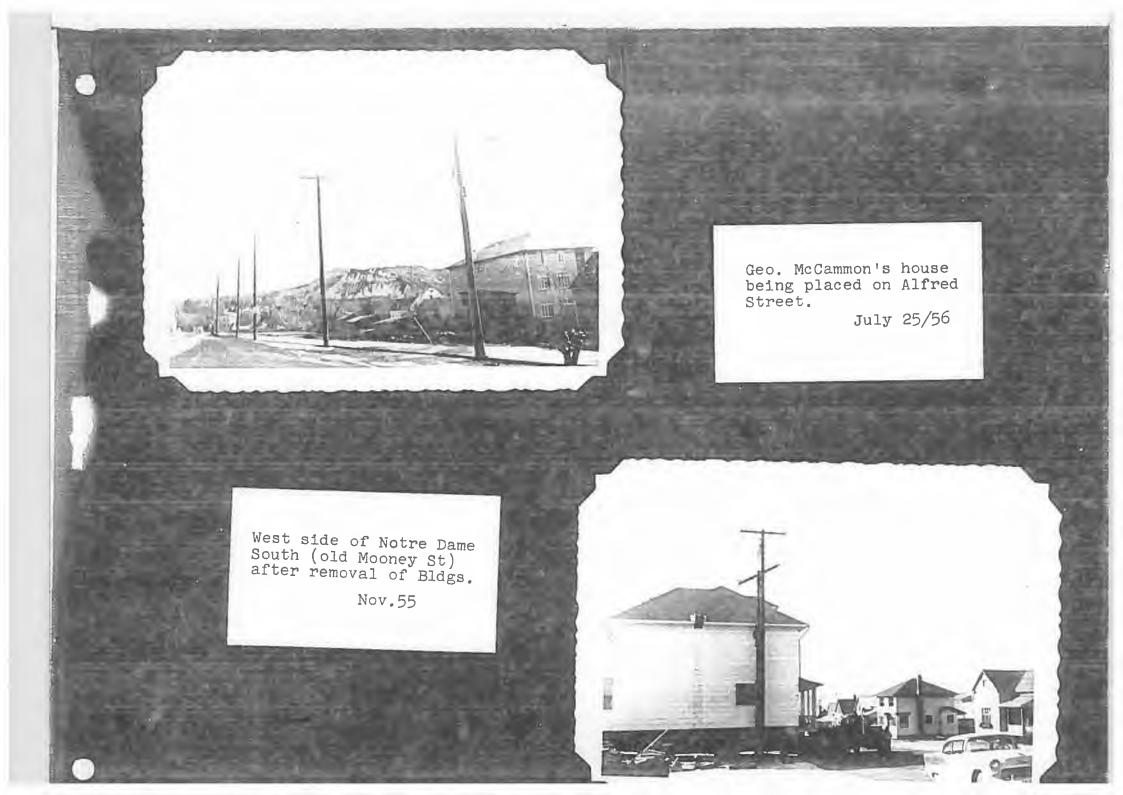


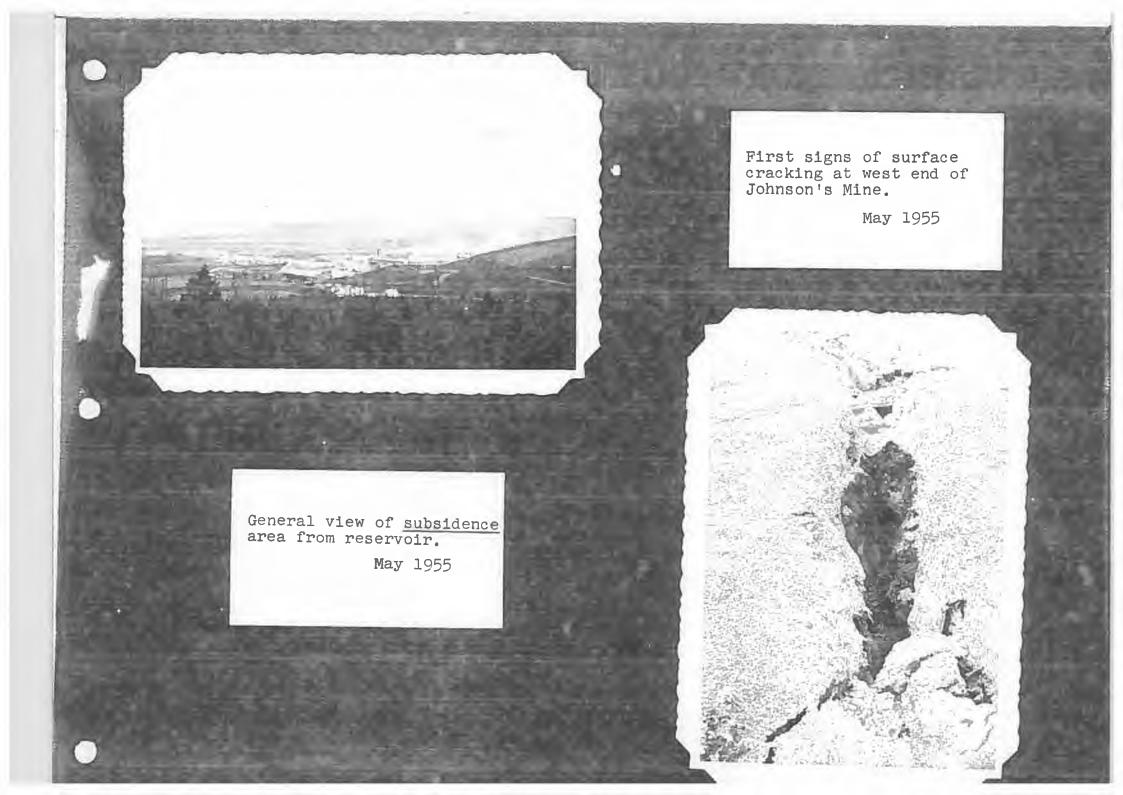


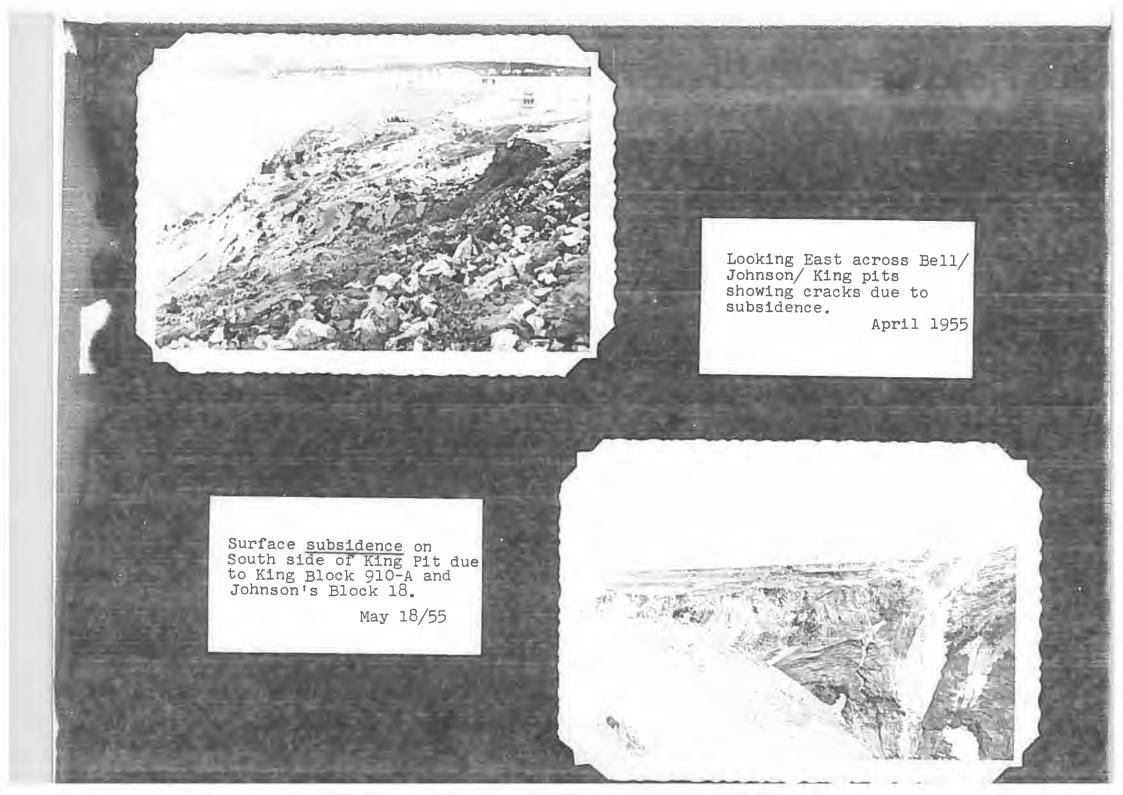


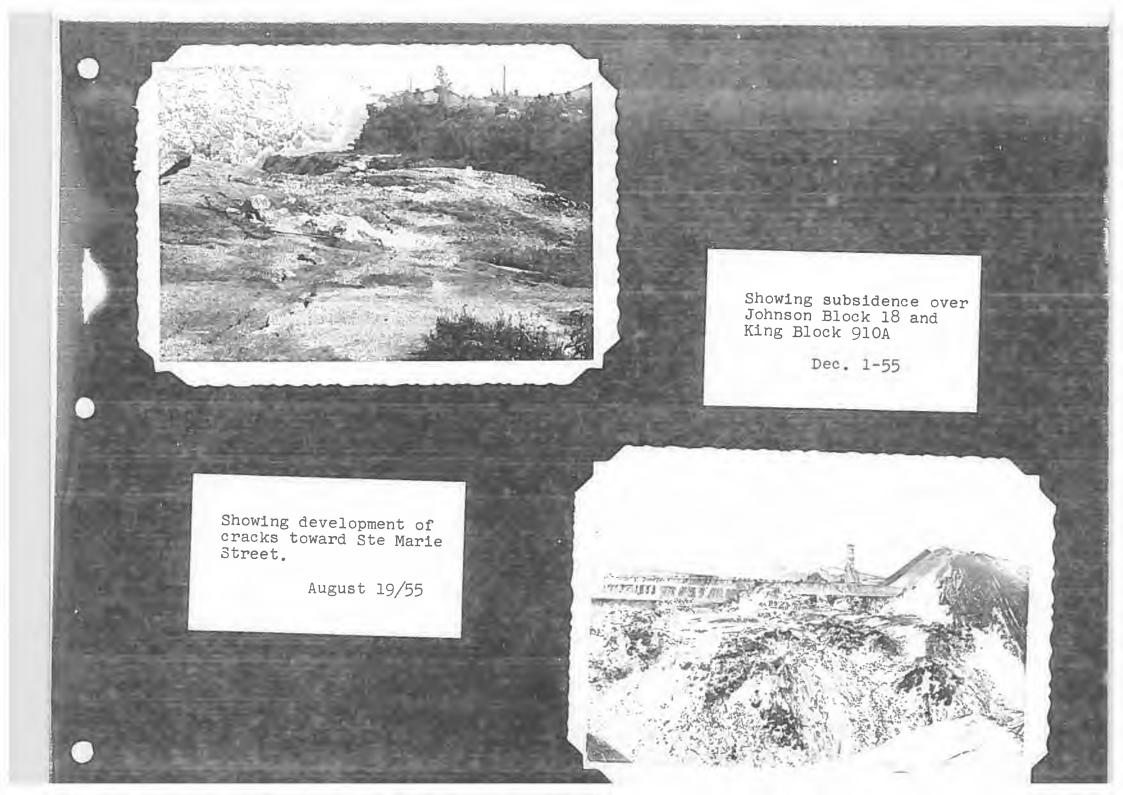


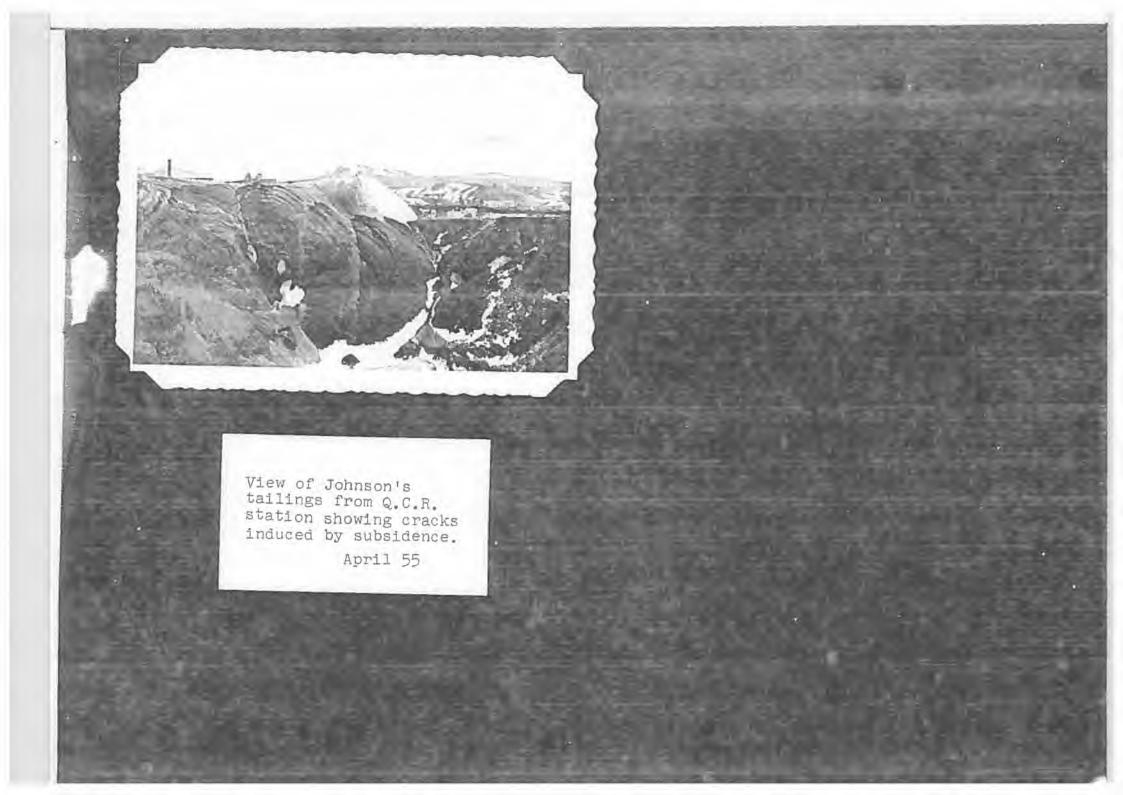

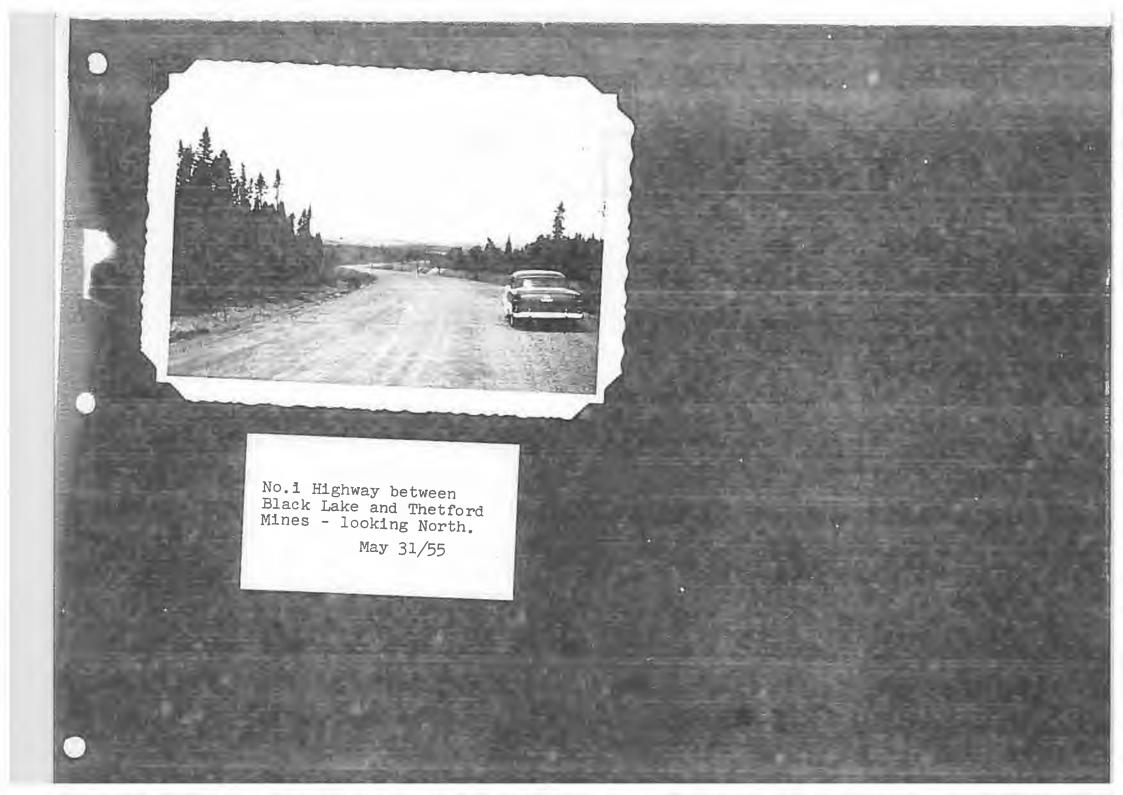

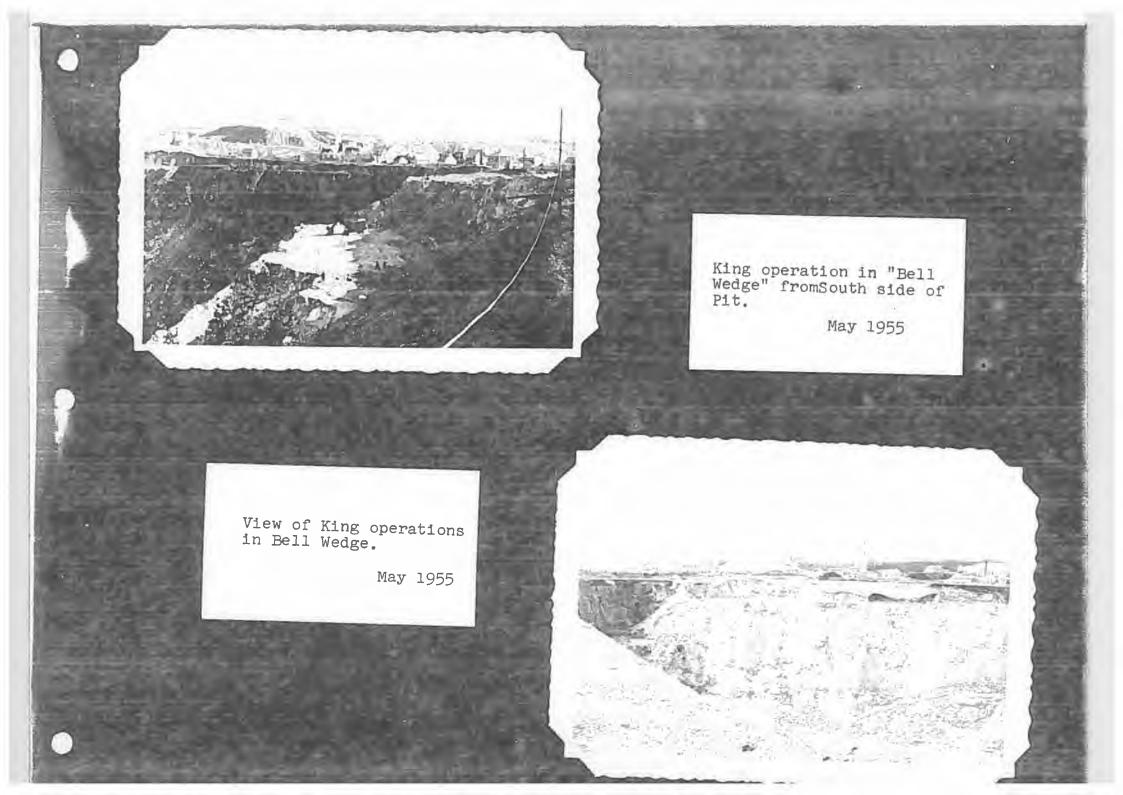


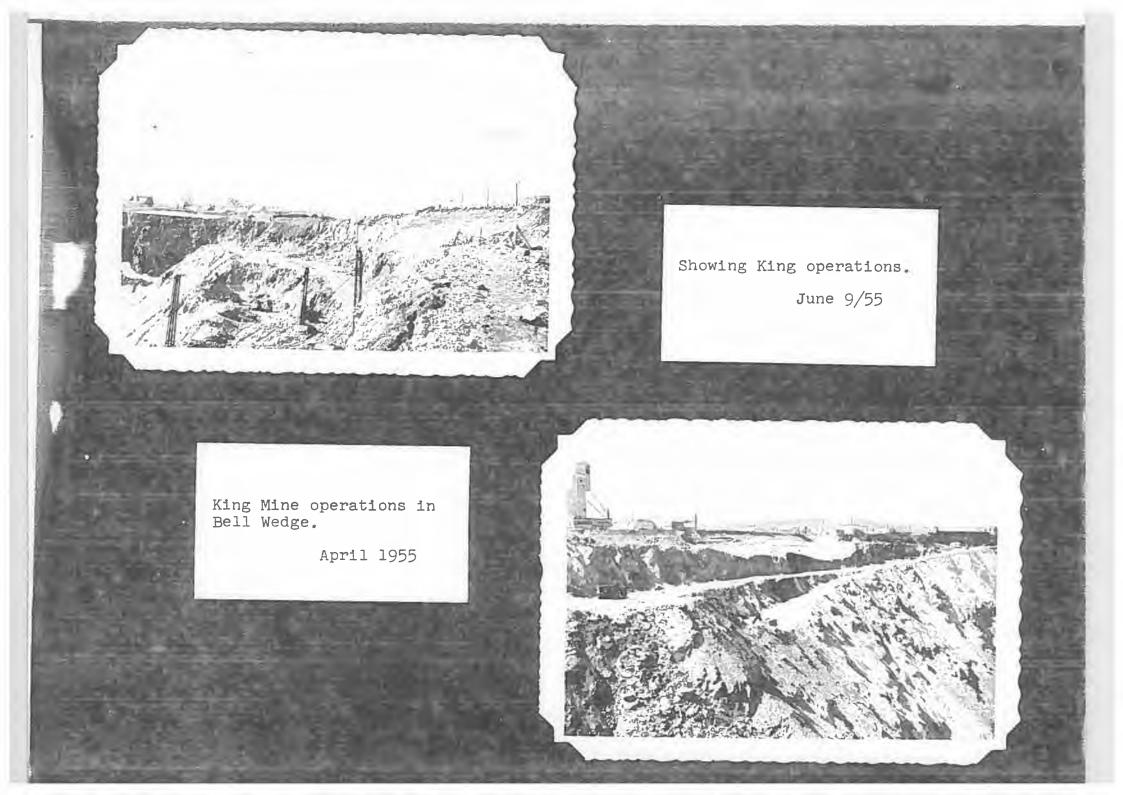


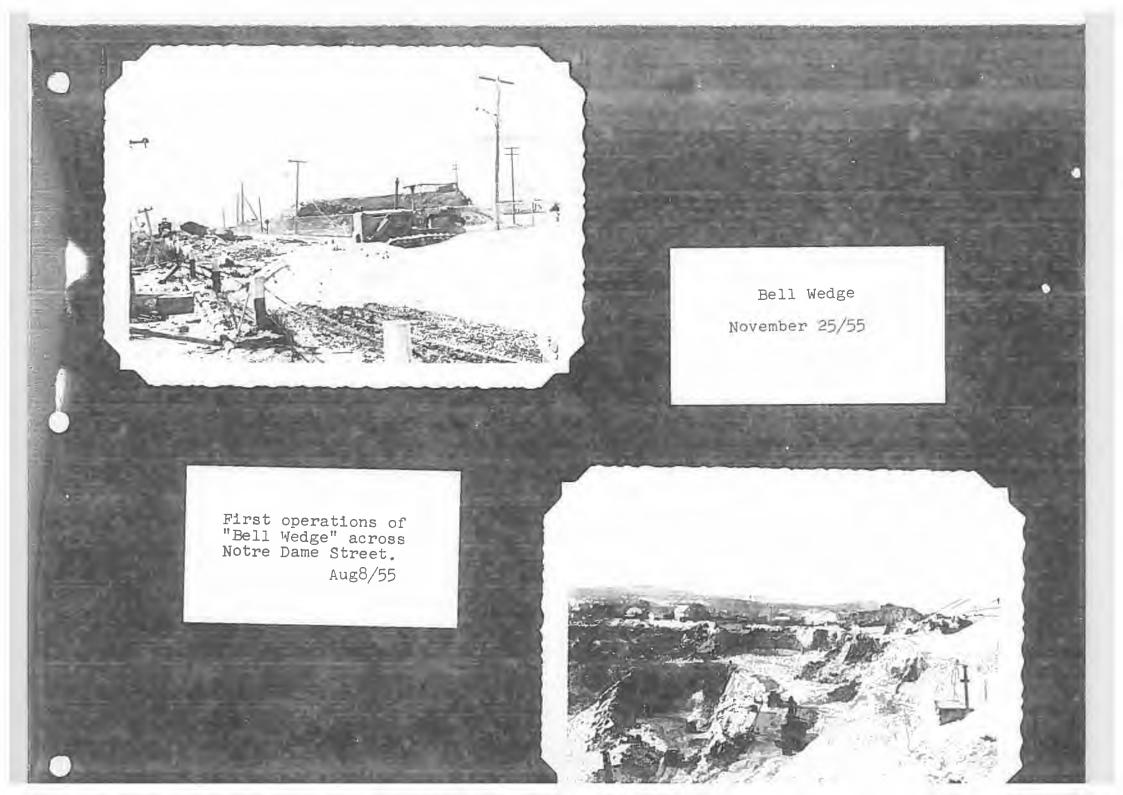








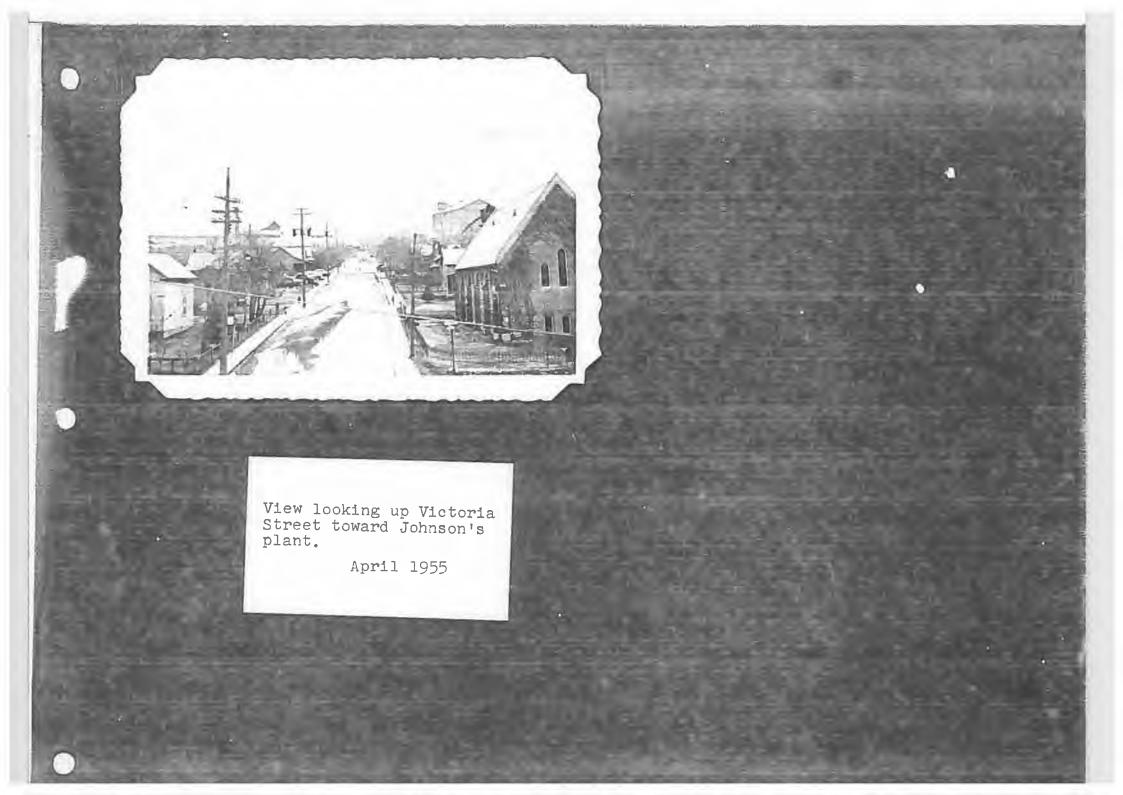


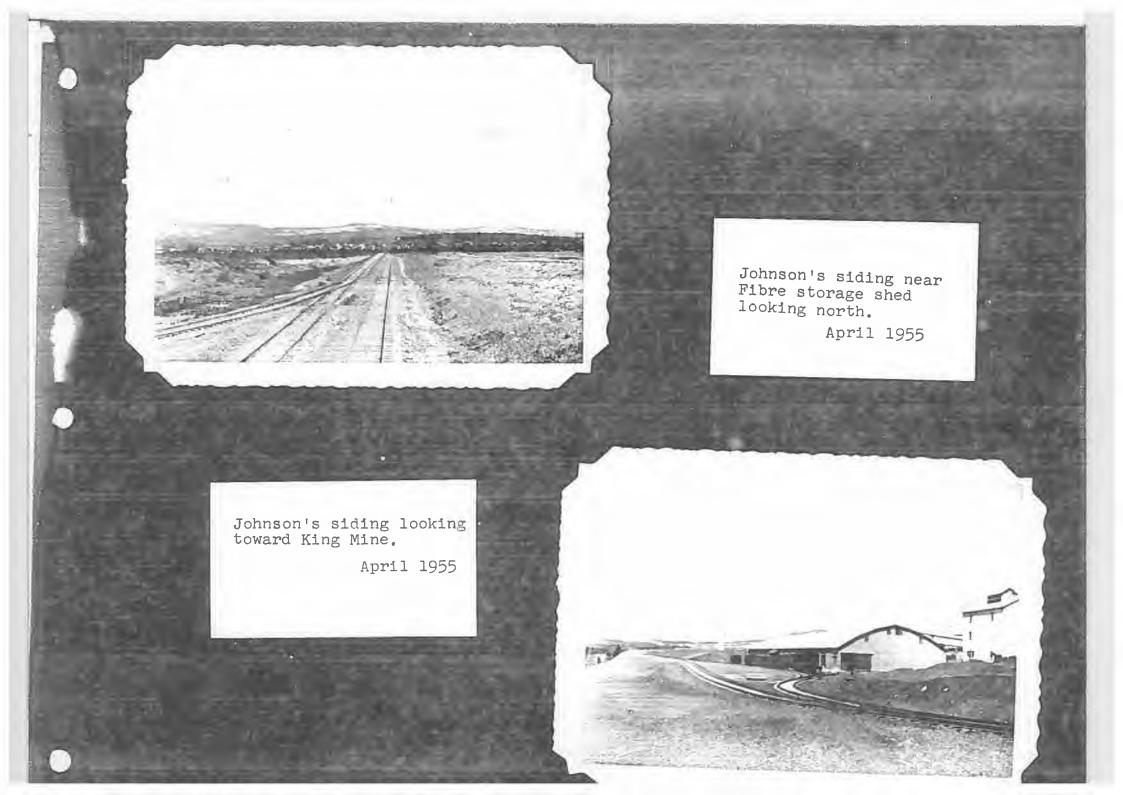


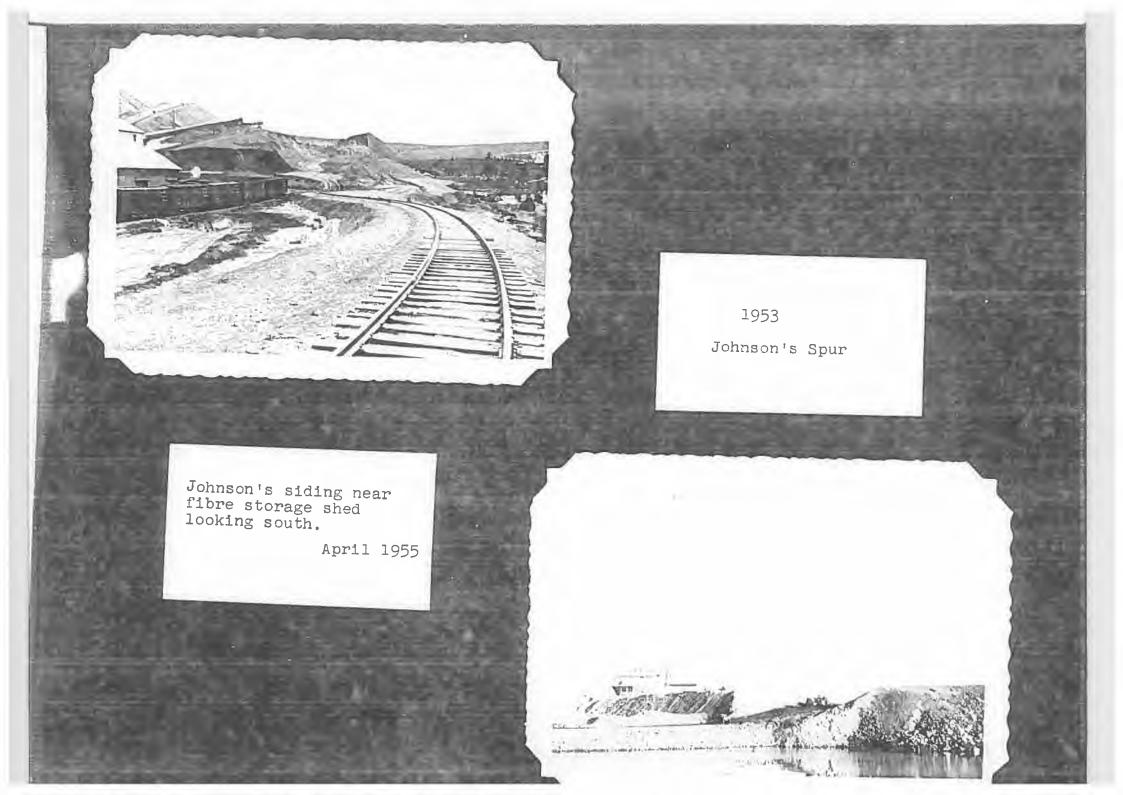


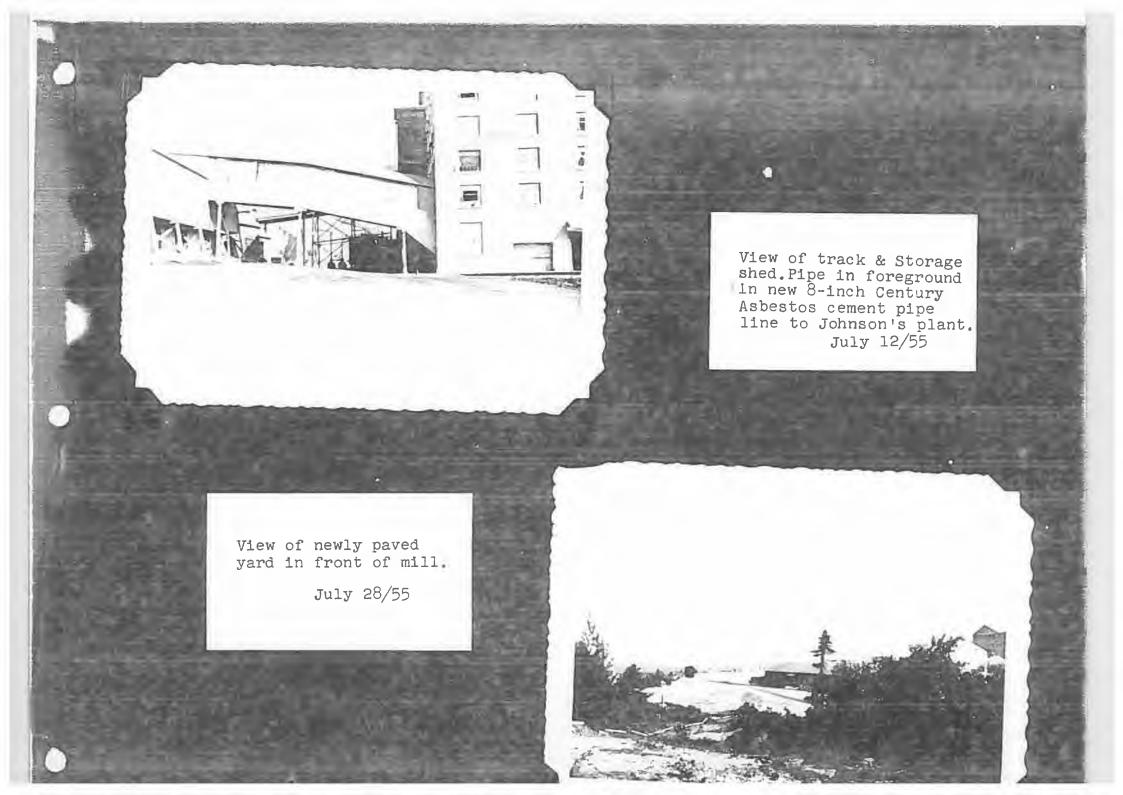


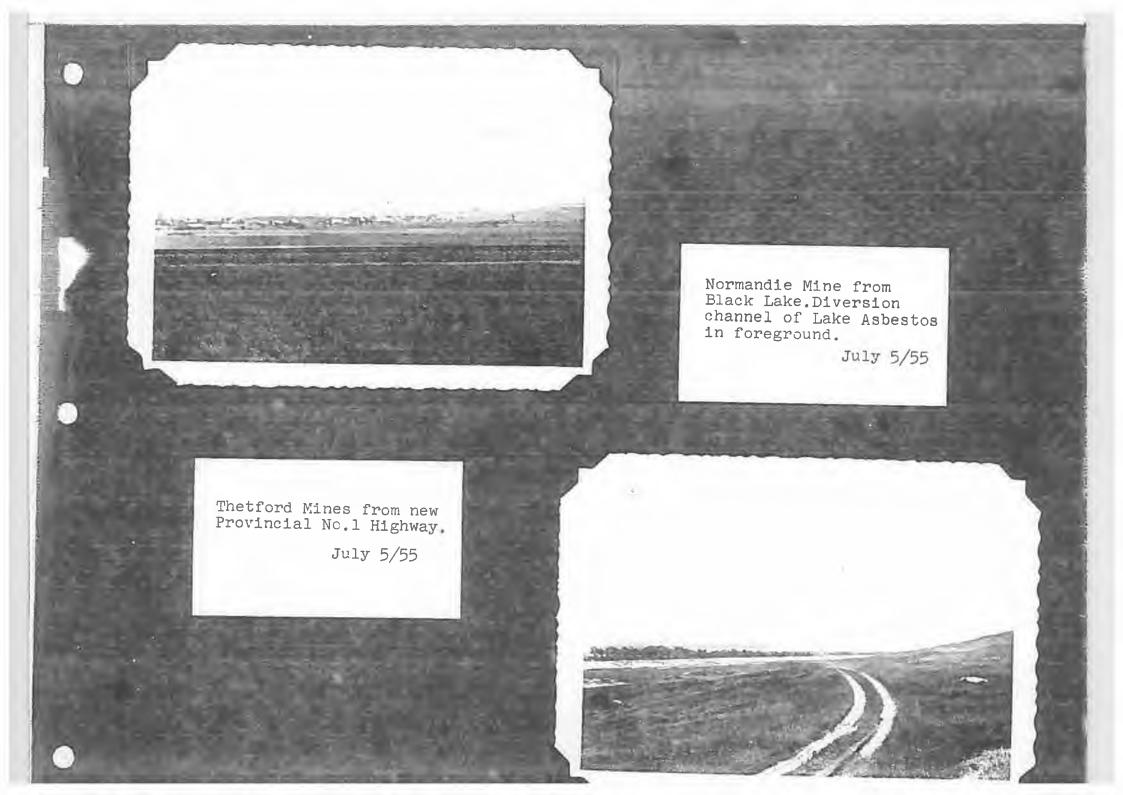

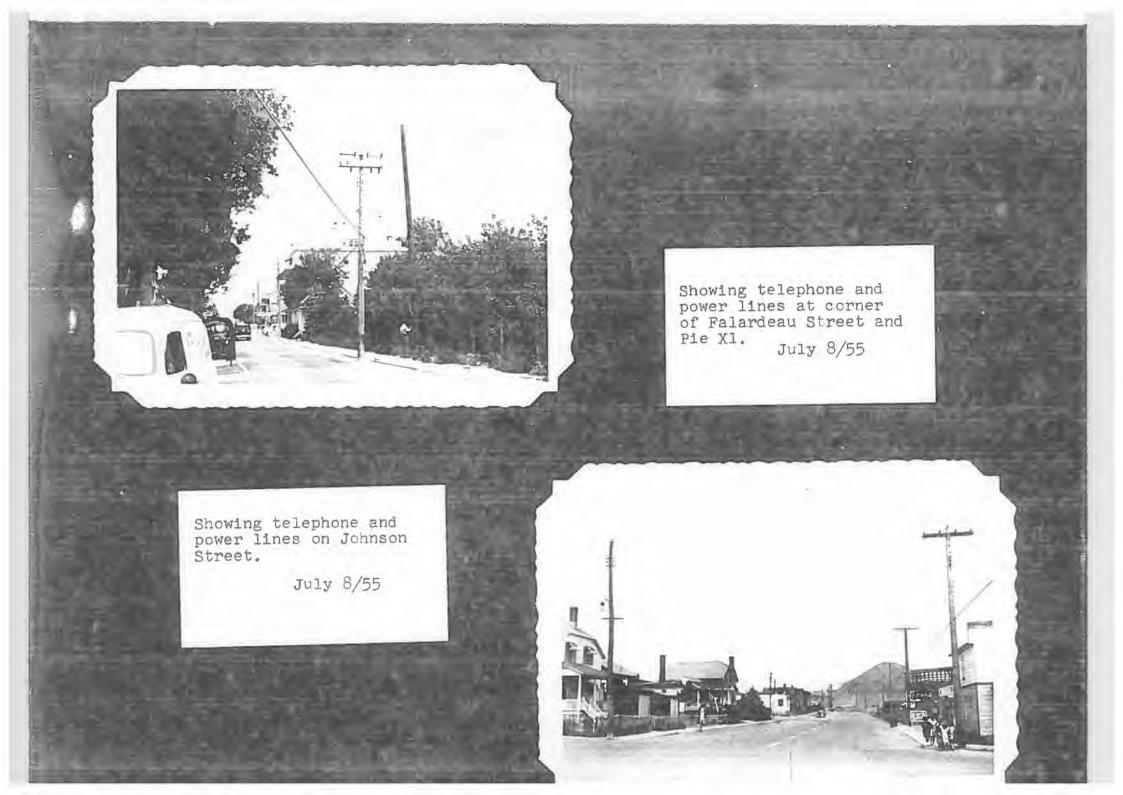


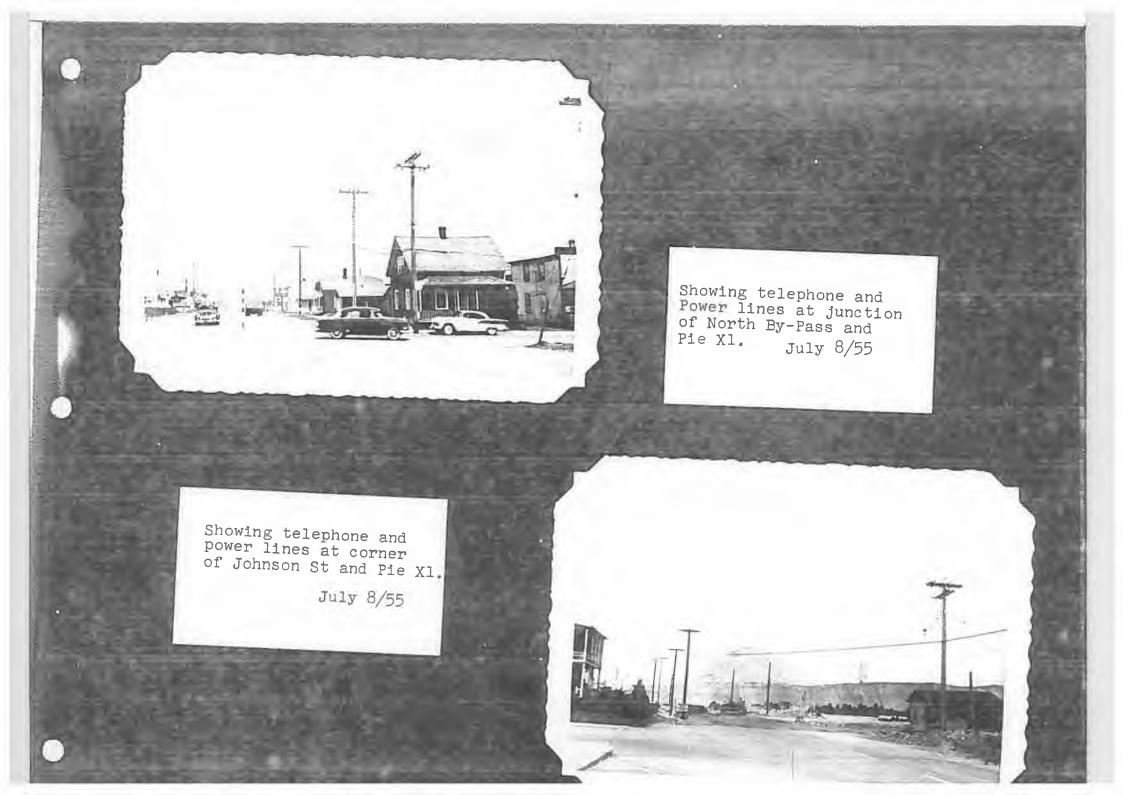

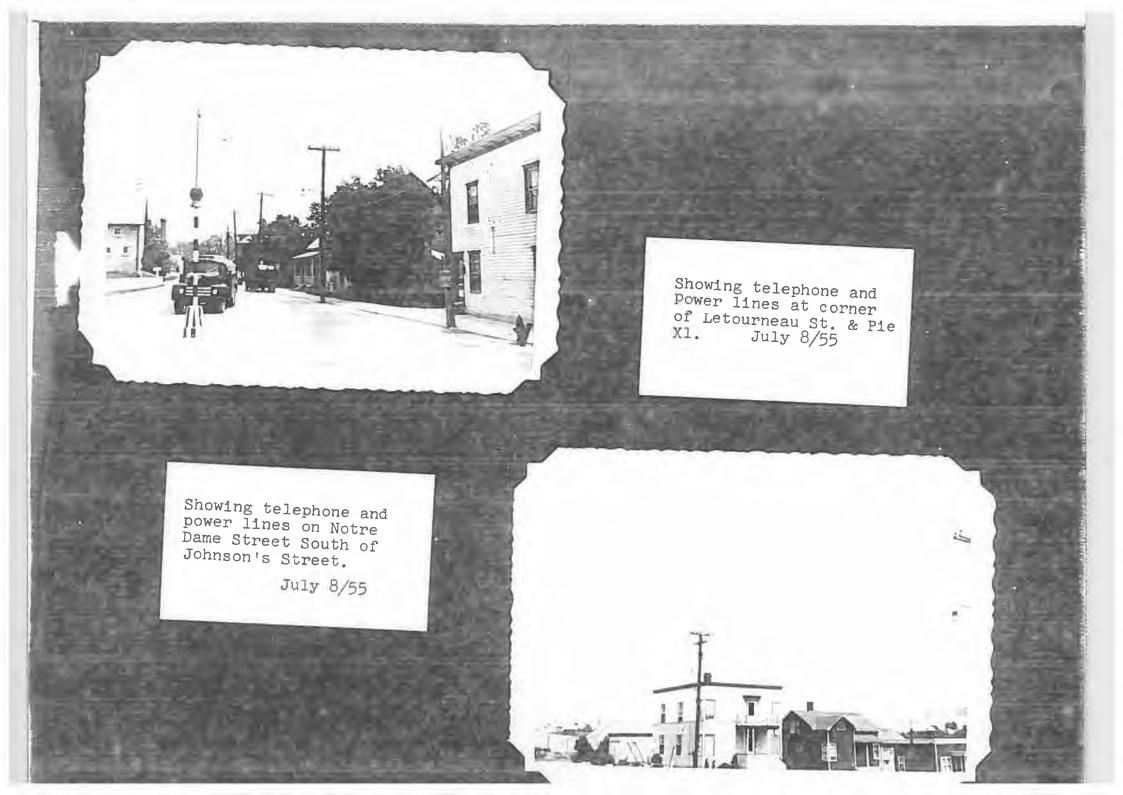

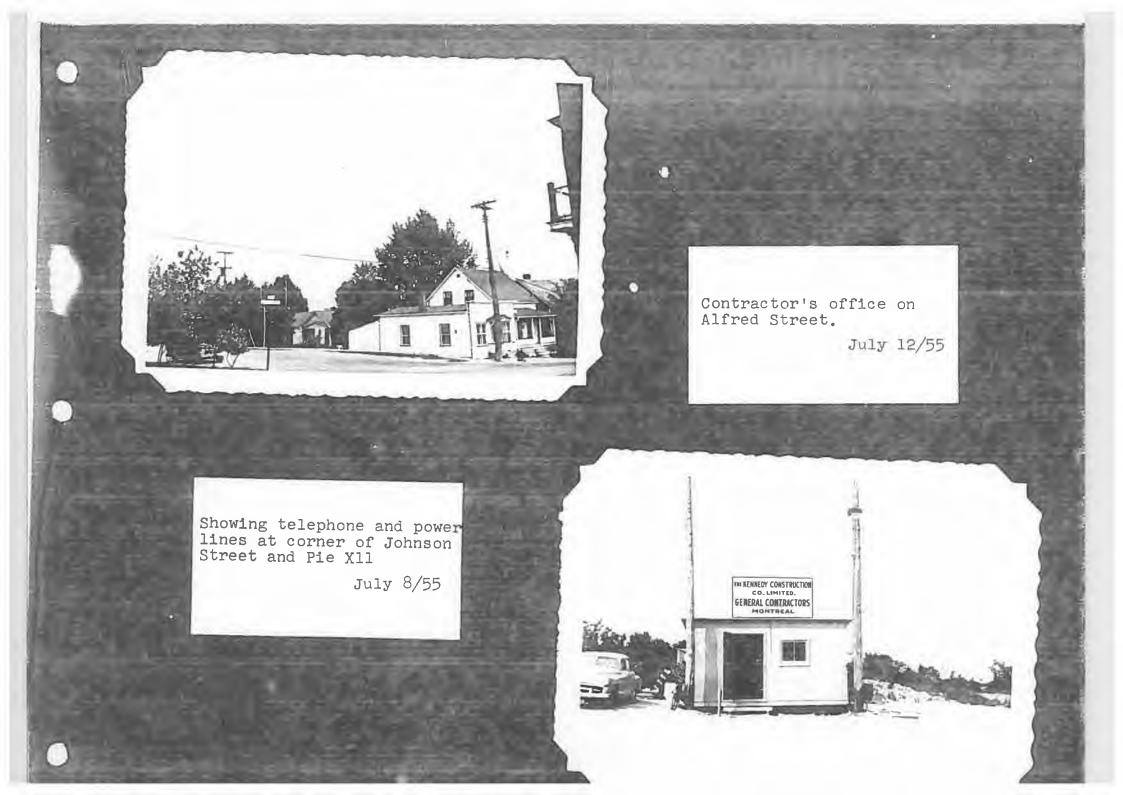



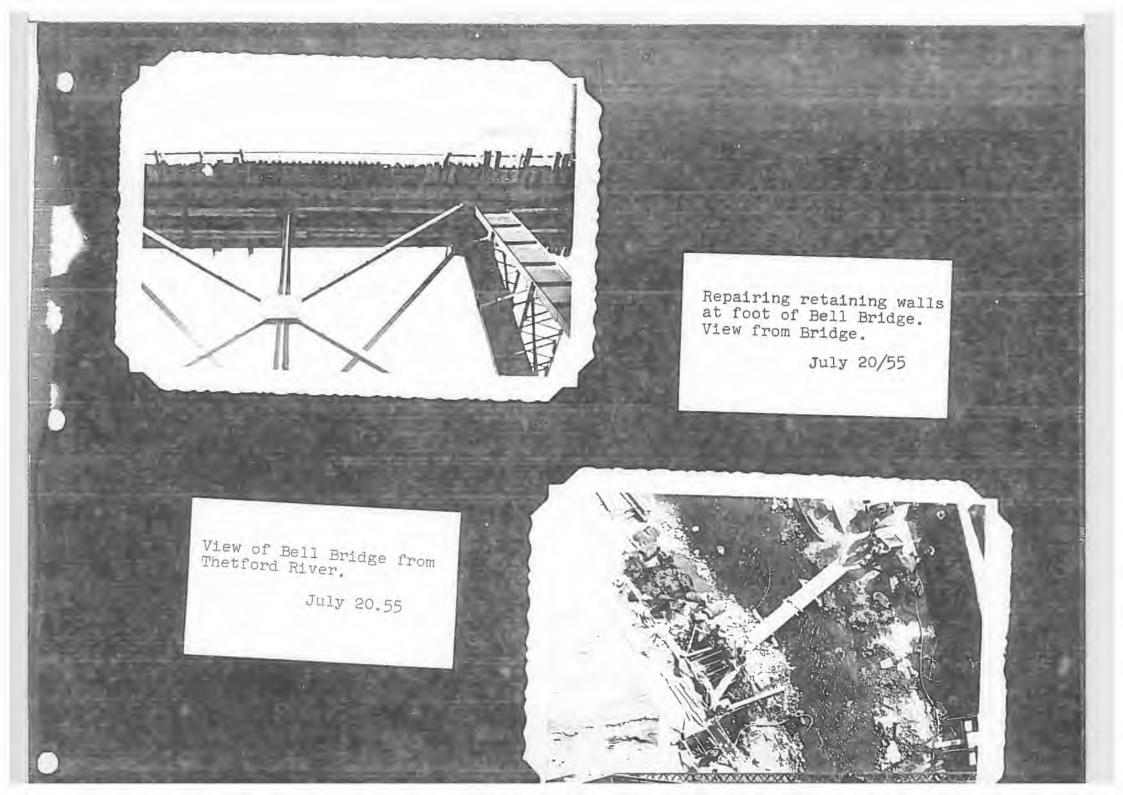



Showing grass strip hetween sidewalk and street paving on Gaudreau St. no curb.

Aug 16/55

Showing method of construction curb on Dubresne Street.

Aug 16/55





